


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 4909
TRUNK HIGHWAY 210
COUNTY Morrison
DISTRICT 3A

LIMITS: In Motley Jct. T.H. 10 - N. end of Bridge (Crow Wing River)

Ref. Pt. 100+00.707 - 100+00.895



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
					No Record of Const: 280' H.T.
		Br. 3012	16'		
1925	210-2-32-2B	Grading Gravel	30' 24'	3"	1400 C.Y./Mile.
1930	210-2-32-2B	Oil Tr. Gravel	30'	1"	10498 Gal./Mile. Maint. Dept.
1935	210-2-36-1A	Grading Br. 5395	32' 27'		300' L.T.
1935	210-2-36-1A	Oil Tr. Gravel	25'	1"	Maint. Dept.
C	4909-03	Plant Mix Bit.	24'	1 1/2" added	
C	4909-04	Regrading Salv. Bit. Base Concrete	38' 24' 22'	2"	1200 C.Y./Mi. 97-9"
C	4909-06	Grading Gravel Base P.C. Concrete	Var.	3/4" 8"	
C	4909-10	Grading Bit. Surfacing	24'	5" 3" 1"	Spec. 2331 Spec. 2341 Spec. 2361
D	8823-100	Agg. Seal			F-2

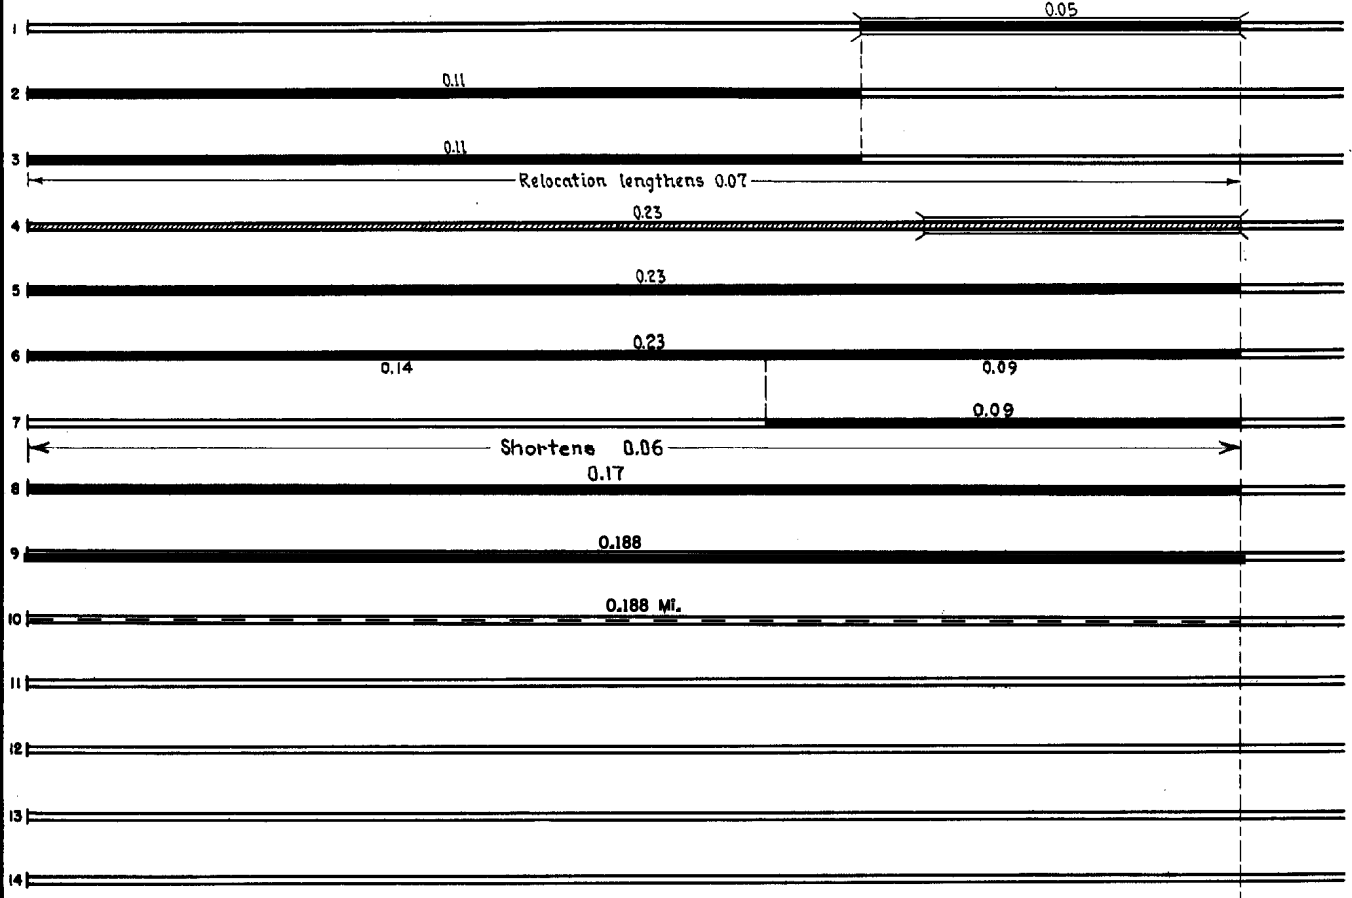

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1925	1934	0.16	0.00	0.00	0.11	0.05	0.11	0.05	0.00	0.00
1935	1964	0.23	0.00	0.00	0.17	0.05	0.17	0.05	0.00	0.00
1965		0.17	0.00	0.00	0.11	0.06	0.11	0.06	0.00	0.00

REMARKS: Layout is to scale as of 1935.

(1) This work not done under these project numbers but lies within the limits of these projects.
