


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0201
TRUNK HIGHWAY 8
COUNTY Anoka
DISTRICT 9A

LIMITS: South Co. Line - East Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1927	8-63-22-B	Grading	38'		
1928	8-16922 D&E	Concrete	27' x 27-9"		
M	1953 A.F.E. 818	Gravel Shoulders			2177 C.V.
M	1955 A.F.E. 619	Profile Correction with Plant Mix Bit.	27'		Plant Mix 342 Tons
M&C	1956 A.F.E. 604 0201-02	Profile Correction with Plant Mix Bit. Traffic Signals	27'		Plant Mix 593 Tons
M	1957 A.F.E. 604	Profile Correction with Plant Mix Bit.	27'		Plant Mix 152 Tons
M	1959 A.F.E. 604	Profile Correction with Plant Mix Bit.	27'		Plant Mix 120 Tons
C	1962 SF 0201-04	Construct Two Right Turn Lanes. Revise Traffic Signals			Pl. Mix Bit. 92 Tons
1968					3.45 Mi. Transferred Out and 2.07 Mi. Trans. to C.S. 0204 (T.H. 49-126)
1969					0.50 Mi. Transferred out in 1969
C	1969 0283-03	Grade, Base, Pl. Mix. Bit. Surf. Pl. Mix. Bit. Shldrs.	24' 10" 3"		10' Rt. & Lt.

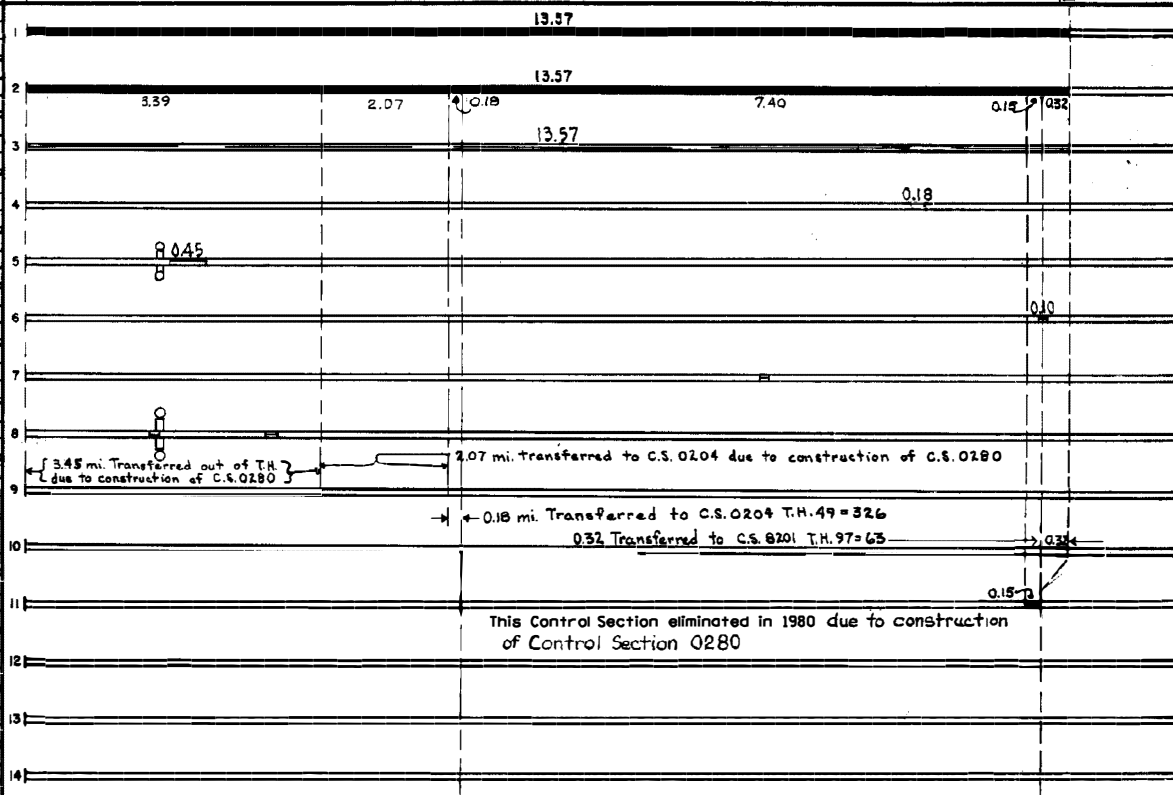

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1927	1949	13.57	13.57	0.00	0.00	0.00	13.57	0.00	0.00	0.00
1950	1950	13.57	12.54	0.00	1.03	0.00	13.57	0.00	0.00	0.00
1951	1953	13.57	11.06	0.00	2.51	0.00	13.57	0.00	0.00	0.00
1952	1954	13.57	10.37	0.00	3.20	0.00	12.88	0.00	0.69	0.00
1955	1959	13.57	5.69	0.00	7.88	0.00	8.20	0.00	5.37	0.00
1960	1968	8.05	5.69	0.00	2.36	0.00	5.69	0.00	2.36	0.00
1969		7.55	5.37	0.00	2.18	0.00	5.37	0.00	2.18	0.00

REMARKS: Layout is to scale as of 1927
