


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2301
TRUNK HIGHWAY 16
COUNTY Fillmore
DISTRICT 6A

LIMITS: N. Co. Line - Jct. T.H. 74 in Spring Valley
Ref. Pt. 211+00.764 - 215+00.436



YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o
		TYPE	WIDTH	THICKNESS	REMARKS	
1921		Grading (1) Gravel	24'	2"		
					Maint. Dept.	
1921	16-9-18	Concrete				
1931	16-9-30-4	Grading Br. 5141	40'	30'		B.S. & W.P.T.-U.P.
1932	16-9-30-4	Gravel	30'	1 1/4"		800 CY./Mile.
1933	16-9-30-4	Concrete	20'	9-7-9		
C	1963 2301-04	Gravel Sub-base Plant mix bit base Plant mix bit surf.	12" 5" 24'	12" 5" 4 1/4"		Sub-base & base 3' ft. All of p.c. conc. in p. Over p.c. conc. in p.
C	1963 2301-02	Grading Sub-base & Crushed rock base Plant mix bit	44'	12" 6" 3"		Rt. & lt. of p.c. Conc. in place Over p.c. conc. in p.
C	1964 2301-05	Lighting System				
M	1966 C	Light Bit Seal	25'			CRS-1 Bit 7114 Gal. FA-1 Agg. 258 Ton
M	1980 SF	Bit. Overlay	22'	1 1/2"		Tack .035 1329.87 Ton (Portion CS 2302)
C	1983 2301-07 F 009-3(40)	Grading Bit. Surface	28'	3"		Remove Old PCC
C	1995 2302-16	Bit. Milling Bit. Overlay	4'	1 1/2" 2 1/2"		Spec. 2341
C	1999 2301-11	Milling Bit. Overlay	24'	1 1/2"		Spec. 2350
M	2001 8826-15	Route & Seal				

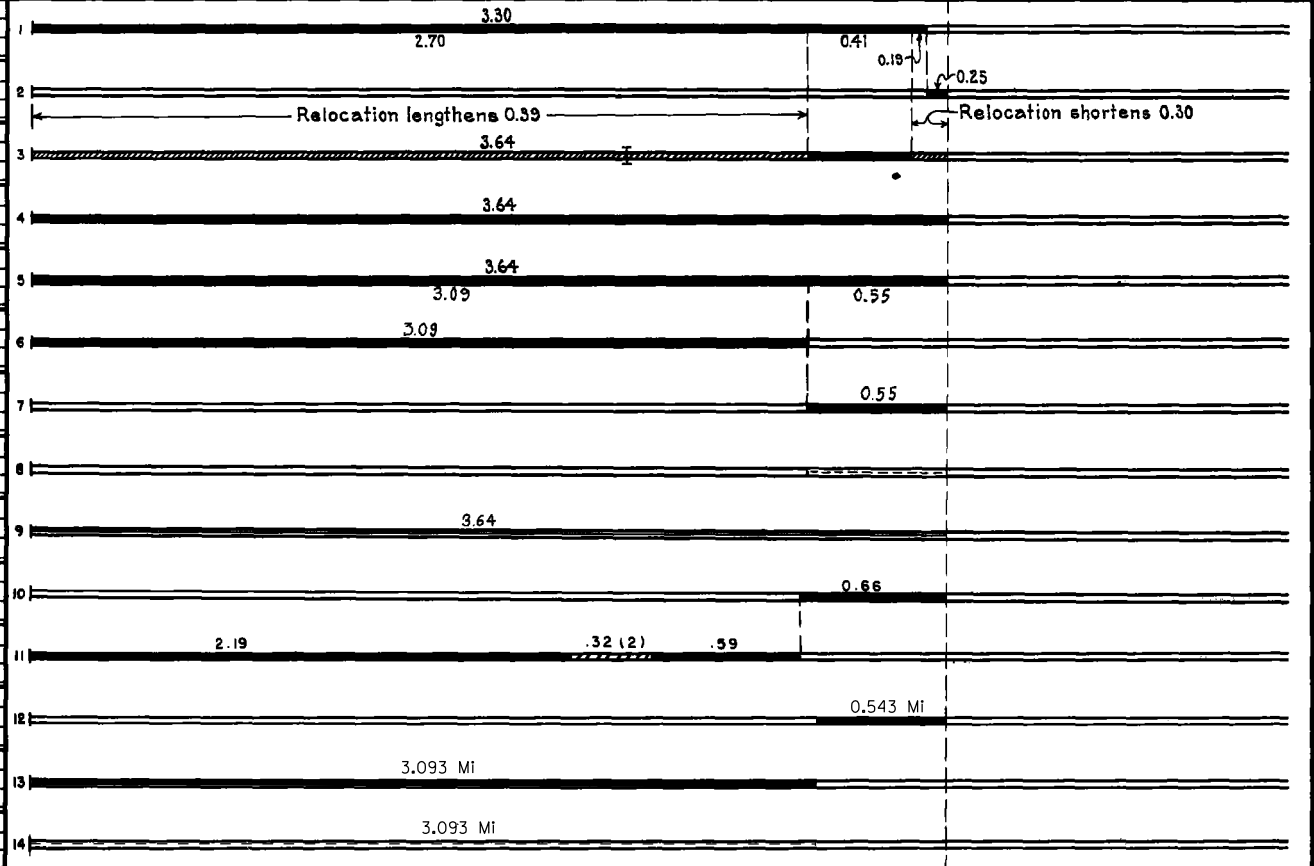

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1930	3.55	2.33	0.00	1.22	0.00	2.33	0.00	1.22	0.00
1931	1961	3.64	3.09	0.00	0.55	0.00	3.09	0.00	0.55	0.00
1962	1973	3.64	2.69	0.00	0.95	0.00	2.69	0.00	0.95	0.00
1974		3.64	2.38		1.26		2.38		1.26	

REMARKS: Layout is to scale as of 1931

(1) No record of constn. of grading

