


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2612
TRUNK HIGHWAY 78
COUNTY Grant
DISTRICT 4B

LIMITS: Main & Melby in Ashby - E. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr.
					Added In 1934.
		Br. 6259	20'		No Record of Constr.
					212' T.P.G. & W.P.T.-O.H.
					Added In 1934.
1921		Grading	24'		Co. Job 1910.
		Gravel	20'	3 1/2"	1300 C.Y./Mile.
					Added In 1934.
1933	A.F.E. 41	Regrading	28'		
	A.F.E. 42	Graveling	28'	1 1/4"	700 C.Y./Mile.
					Maint. Dept.
M					Gravel & Clay
1941	A.F.E. 9	Regraveling & Consolidation			388 C.Y./Mi.
					Maint. Dept.
C					MC-2, 8044 Gal./Mi.
1945	A.F.E. 4	Bit. Surf. Treat.	20'	3/4"	Grav. 341 C.Y./Mi.
					Maint. Div.
M					
1951	A.F.E. 6	Grav. Resurfacing			476 C.Y.
M					
1952	A.F.E. 6	Grav. Resurfacing			196 C.Y.
M					
1953	A.F.E. 604	Bit. Surf. Repair	24'		SC-3, 2865 Gal.
					Agg. 141 C.Y.
C					
1954	2612-02	Grading Gravel	26' 26'	3/4" 1 1/2"	700 C.Y./Mi.
C					
1955	2612-03	Stab. Sand-Gr. Sub-base Stab. Grav. Base Plant Mix Bit.	30' 30' 24'	0'-6" 3" 1 1/2"	
M					
1956	A.F.E. 605	Light Bit. Seal	24'		RS-2, 4846 Gal.
					Agg. 160 C.Y.
C					
1968	2612-05	Grading Base & Pl. Mix. Bit. Surf.	43' 24'	6" 2"	Bit. Mat'l. 57 Ton
					Br. 26001
M					
1981	2612 SF	Bit. Surfacing Aggregate Shldr.	24' 9'	3" Var.	

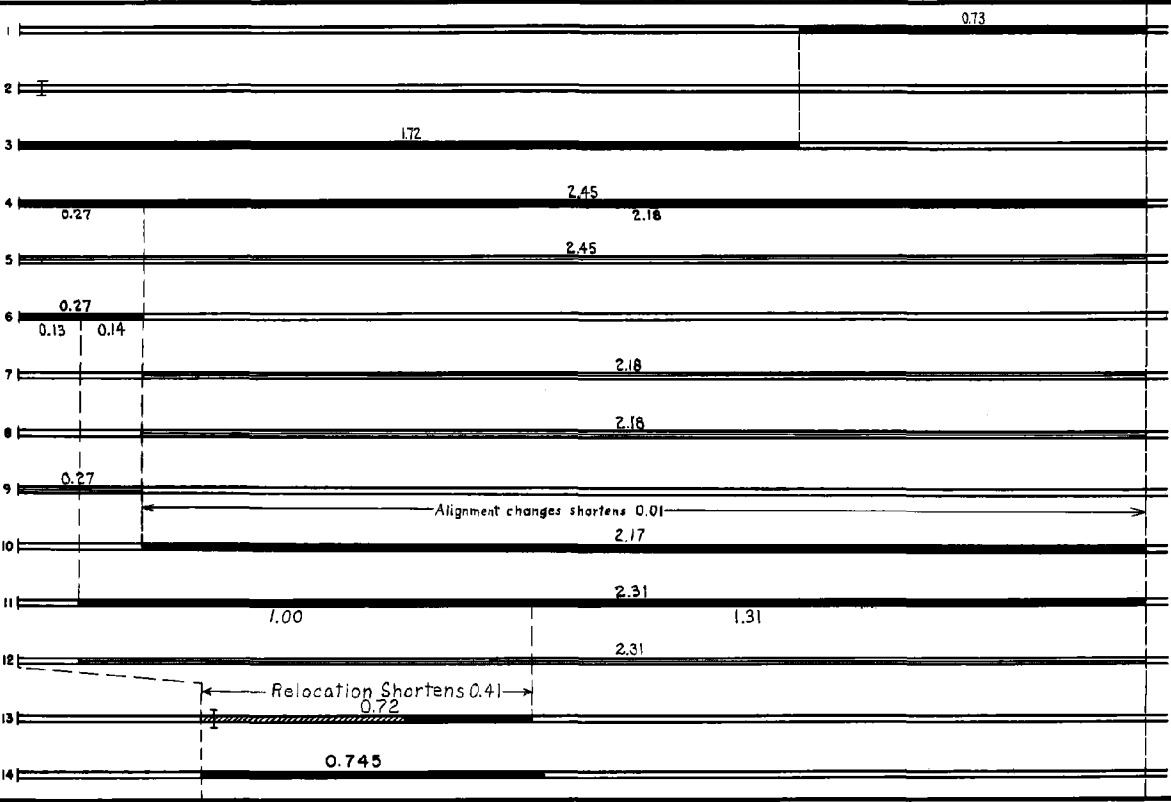

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1953	2.45	2.18	0.00	0.23	0.04	2.41	0.04	0.00	0.00
1954	1964	2.44	2.17	0.00	0.23	0.04	2.40	0.04	0.00	0.00
1965		2.44	2.18	0.00	0.22	0.04	2.40	0.04	0.00	0.00

REMARKS: Layout is to scale as of 1934.

