


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3406
TRUNK HIGHWAY 5
COUNTY Kandiyohi
DISTRICT 8A

LIMITS: W. Jct. T.H. 104 at W. Co. Line - Jct. T.H. 71



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
					No Record of Constr.
		Gravel	24'	2"	Added in 1934.
					No Record of Constr.
		Gravel	18'	1/2"	Added in 1934.
1930		Grading	24'		Co. Job 3002 B.
		Gravel	18'	2"	1000 C.Y. / Mile. Added in 1934.
1935	23-143-21	Gravel	22'	2"	Relief Labor.
1935	23-210-22-2	Gravel	22'	1/4"	Relief Labor.
(1)					
1936	23-143-21	Oil Tr. Gravel	24'	1"	12000 Gal. / Mile. Maint. Dept.
1936		Oil Tr. Gravel	24'	1"	Maint. Dept.
M	1940 A.F.E.10	Regraveling			314 C.Y. / Mile. Maint. Dept.
M	1943 A.F.E.4	Spot Treat. Bit. Surf. Repair			Oil, 26758 Gal. / Mi. Grav. 1577 C.Y. / Mi. Maint. Dept.
M	1943 A.F.E.6	Grav. Resurface			304 C.Y. / Mi. Maint. Dept.
C	1944 3406-02	Grading	26'		
C	1944 A.F.E.23	Gravel Surface			561 C.Y. / Mi. Maint. Div.
M	1944 A.F.E.4	Bit. Surf. Repair			Oil, 7983 Gal. / Mi. Grav. 250 C.Y. / Mi. Maint. Div.
M	1946 A.F.E.6	Grav. Resurfacing (Spot)	20'		462 C.Y.

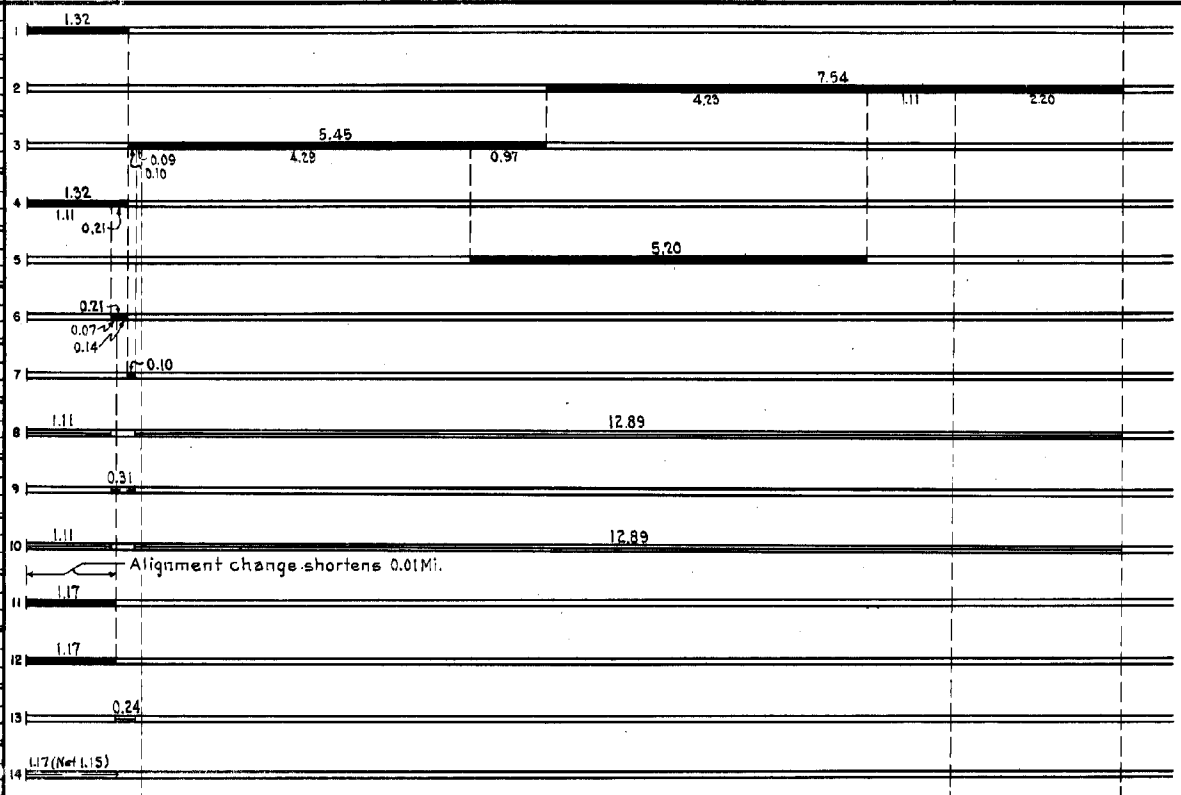

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1943	14.31	14.31	0.00	0.00	0.00	14.31	0.00	0.00	0.00
1944	1950	14.30	14.30	0.00	0.00	0.00	14.30	0.00	0.00	0.00
1951	1955	14.30	13.63	0.00	0.67	0.00	14.30	0.00	0.00	0.00
1956		12.43	11.91	0.00	0.52	0.00	12.43	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934.

(1) This work not done under this project number but lies within the limits of this project.

