

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3601
TRUNK HIGHWAY 1
COUNTY Koochiching
DISTRICT 2A

LIMITS: W. Co. Line - S. Jct. T. H. 71

Ref. Pt. 147+00.471 - 151+00.288

YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° DIST
		TYPE	WIDTH THICK- NESS	REMARKS	
		Br. 8013 Gravel	16' 18' 3/4"	14' Wood Span. No Record of Constr. Added in 1934.	
C 1940		Br. 8013	22'	Br. Widening. 14' Wood Span. Gang # 3.	
C 1941	A.F.E. 23	Regrading Graveling Culvert	28'	1045 C.Y./Mi. Maint. Dept.	
M 1946 1947	A.F.E. 6	Grav. Resurfacing		4850 C.Y.	
C 1947	A.F.E. 24	Grading & Graveling	28'	1040 C.Y.	
M 1950	A.F.E. 6 A.F.E. 31	Gravel Resurfacing Spot Swamp Fills & Ditch Cleaning	24' 6" 12"	5336 Tons	
C 1952	3601-03	Grading Gravel	28' 26' 2"	1.0' Select Mat'l (except 1.0' Sand-Grav. Subbase Mi. Pt. 3.69-3.91)	2.51
M 1956	A.F.E. 606	Grav. Resurfacing	24'	1947 Tons	
C 1961	3601-04	Grading Sub-base & Base* Plant Mix Bit. (Base)	42' 32' x 3" 24' 1 1/2"		161 456
M 1966	C	Light Bit. Seal	25'	RC-250, 6880 Gal. Agg. 258 C.Y.	1066
C 1968	3601-06	Pl. Mix. Bit. Surf. Gravel Shldrs.	24' 3"	Bit. Mat'l. 497 Ton 4' Rt. & Lt.	168
M 1983	SF	Spot Bit. Overlays	24' 1 1/2"	Pl. Mix 2331-853 Tons Total In CS 3601A 0405	
M 1988	M 4271	Bit. Overlay	28' 1 1/2"	Spec. 2331	
C 1989	3601-07	Grading Bit. Surfacing	3 1/2' 24' 1 1/2"	Spec. 2331 Spec. 2341	

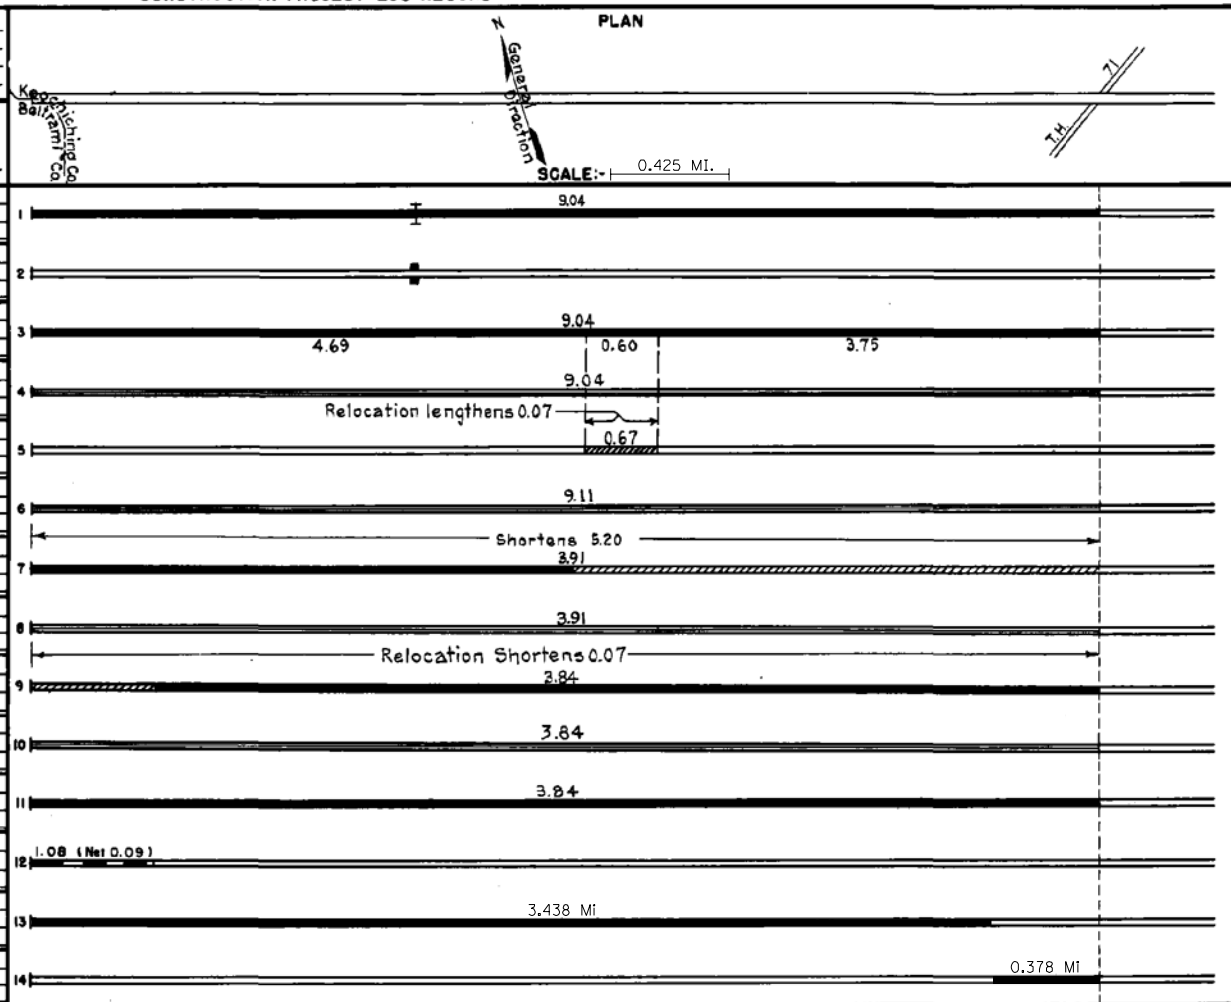

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1946	9.04	8.58	0.00	0.46	0.00	9.04	0.00	0.00	0.00
1947	1951	5.11	8.65	0.00	0.46	0.00	9.11	0.00	0.00	0.00
1952	1960	3.91	3.91	0.00	0.30	0.00	3.91	0.00	0.00	0.00
1961		3.84	3.84	0.00	0.00	0.00	3.84	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934

