

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4510  
TRUNK HIGHWAY 219  
COUNTY Marshall  
DISTRICT 2B

LIMITS: S. Co. Line - Jct. T.H. 89

Ref. Pt. 003+00.507 - 015+00.401

YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION				CODE N <sup>o</sup> DIST
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel	28'		No Record of Const. Added in 1949	
		Br. 6911, 6912 & 6913	17'		41'A Truss, 10' B.S. & 16' B.S.	
M	1951 A.F.E. 6	Grav. Resurfacing			6185 Tons	
C	1953 4510-03	Grading	28'			
(1)		Select Soil Subbase	28'	9"		853
		Gravel Base	28'	3"		
C	1954 A.F.E. 820	Bit. Surfacing			SC-3, 127476 Gal.	
(1)	4510-04	Mixed Bit. (Mixed Pr.)	24'	1"	Agg. 8400 Tons	
		Br. 6911, 6912 & 6913	30'		36' B.S., 20' C.S. & 20' C.S.	1153
M	1955 A.F.E. 605	Light Bit. Seal	24'		RC-2 & RS-2, 18272 Gal.	
					Agg. 656 C.Y.	
M	1961	Bit. Surf. Repair	24'		MC-2, 93648 Gal. for	
		Fog Seal Coat	24'		Repair & 16169 Gal. for	
					Tack & Seal	
C	1971 4510-06	Plant Mix Bit.	24'	1 1/2"		2569
		Gravel Shoulders	3'	Var.		
C	1973 4510-07	PLATE BEAM GUARD RAIL FOR BR 6911, 6912 & 6913			701 LIN. FT.	1473
C	1988 4510-11	Bit. Overlay	24'	1"	Spec. 2331	
				1 1/2"	Spec. 2341	
S	2009 4510-15	Milling	24'	1 1/2"		
		Bit. Overlay	24'	3"	Spec. 2360	

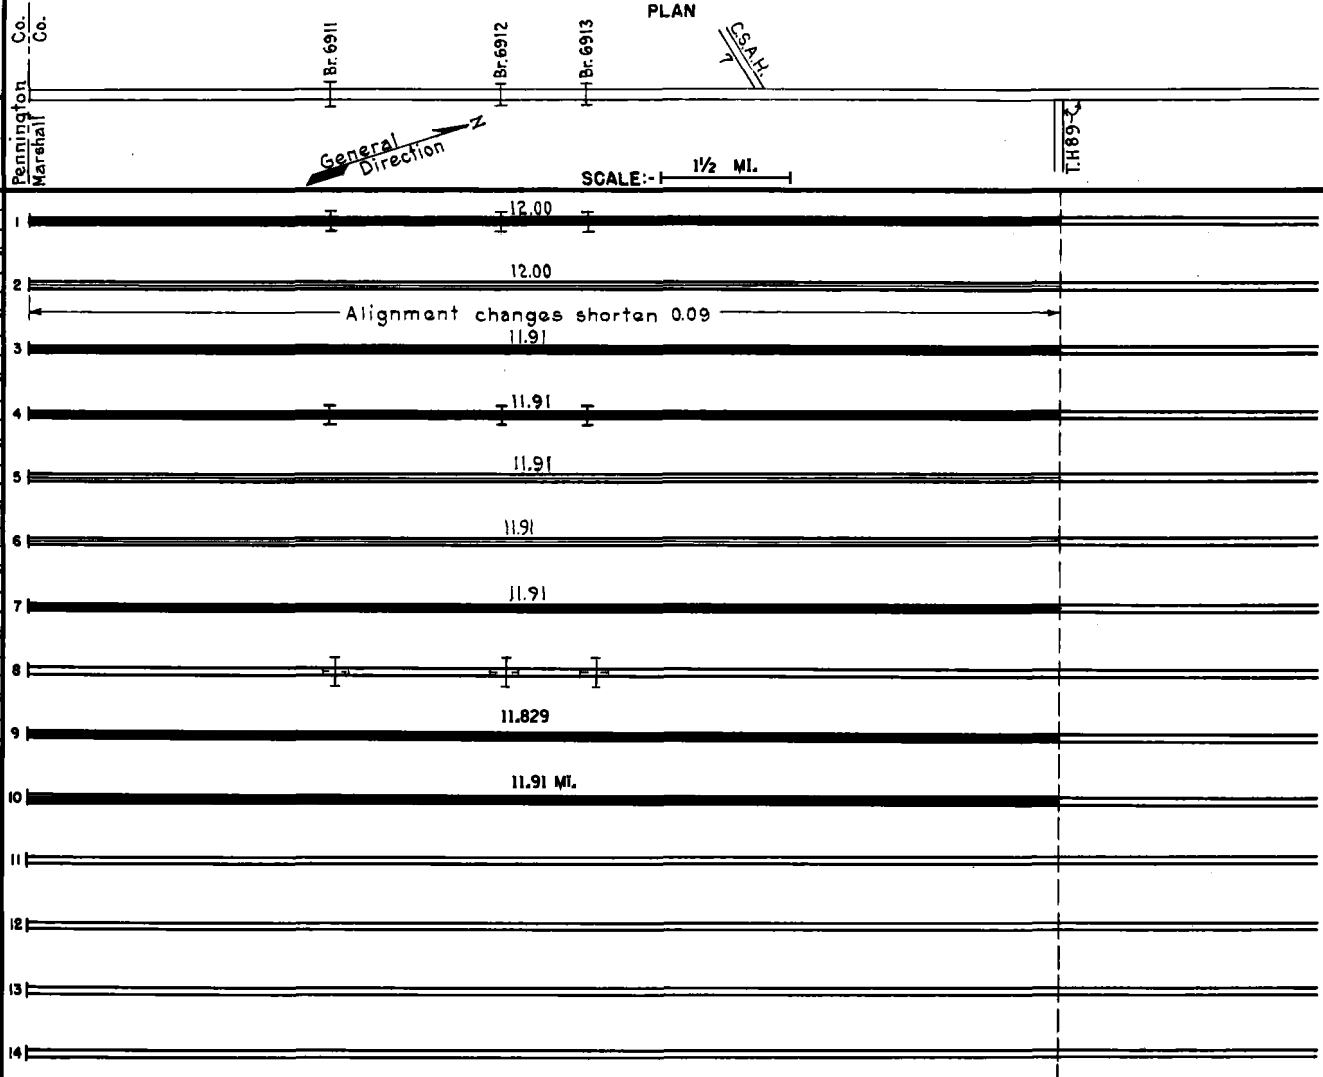

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1952	12.00	11.99	0.01	0.00	0.00	11.99	0.01	0.00	0.00
1953		11.91	11.90	0.01	0.00	0.00	11.90	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1949.  
(1) Contract not final but work substantially complete
