


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4605  
TRUNK HIGHWAY 16  
COUNTY Martin  
DISTRICT 7B

LIMITS: W. Jct. T.H. 4 (State-Aid Road) N. Corp. Limits of Sherburne



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr.
1924	16-9-38	Grading Br. 3923	30' 20'		Contract completed in 1925. 46' B.S.
1924	16-9-38	Gravel	24'	3 1/2"	1600 C.Y./Mile.
1929	16-9-4-1	Grading Br. 4910 Br. 4911	32' 27'		WIDENED. 40' B.S.
1931	16-9-4-2	Regrading Concrete	20'	9-7.9	
1932	16-9-38	Regrading Concrete Br. 3923	20' 28'	9-7.9	(Br. Widening) 46' B.S.
C	1948 A.F.E. 20	Misc. Grading			
C	1954 4605-01	S.C. Pipe Culvert			60'x40'
C	1955 4605-03	Grading Bit. Stab. Base Plant Mix Bit.	44' 44' 24'	6" 3"	On 12" Sand-Gr. Sub-base
M	1971 4605-05	Pl. Mix Bit Resurf.	2 1/2"	2 1/2"	
C	1975 4605-07	Bit. RESURFACING Asp. SURFACE RE. LT.	20' 10'	2 1/4" 2 1/2"	Pl. Mix Bit. 3135 Ton C.I. Agg. 4709 Ton

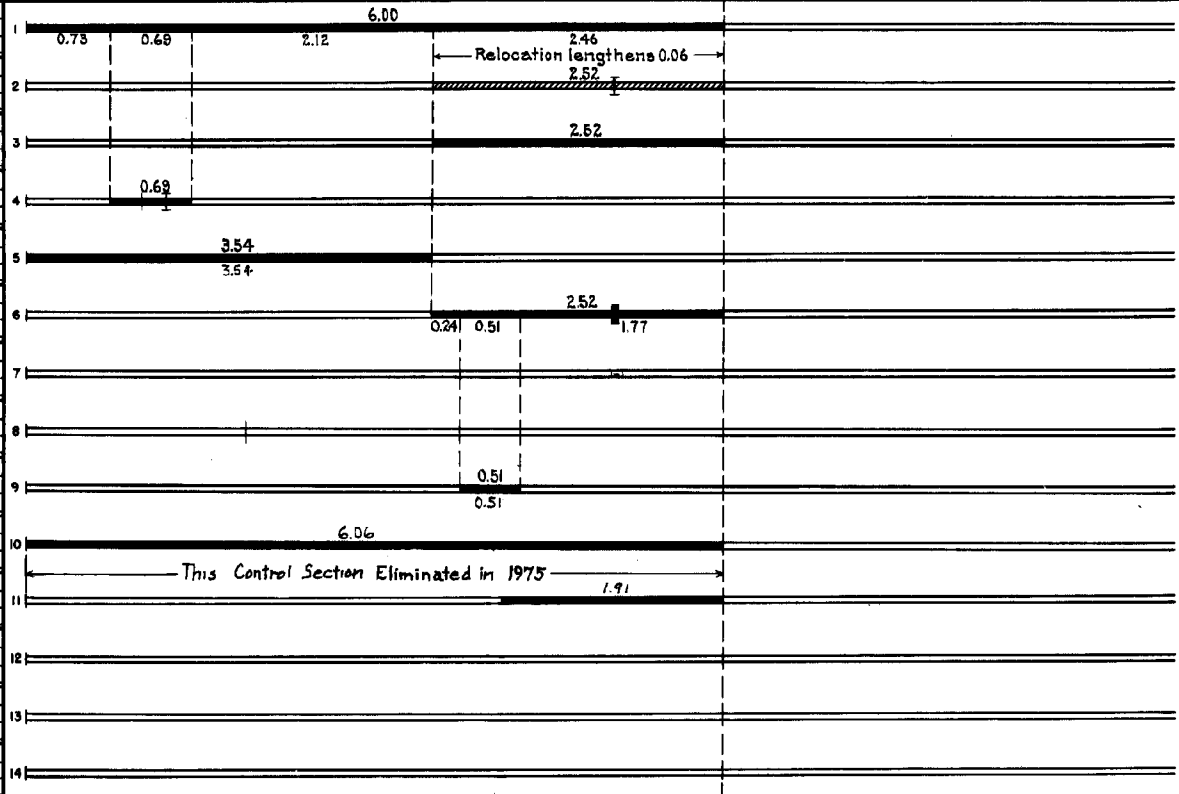

YEARS		TOTAL MILES	UNINCORPORATED				INCORPORATED				RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.		
1921	1923	6.00	6.00	0.00	0.00	0.00	0.00	6.00	0.00	0.00	0.00	0.00	0.00	
1924	1974	6.06	6.04	0.02	0.00	0.00	0.00	6.04	0.02	0.00	0.00	0.00	0.00	
1975		0.00												

REMARKS: Layout is to scale as of 1924

12-75
