


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 5101
TRUNK HIGHWAY 30
COUNTY Murray
DISTRICT 8B

LIMITS: W. Co. Line - W. Jct. T.H. 91 in Lake Wilson

Ref. Pt. 020+00.054 - 025+00.678



YEAR BUILT	PROJECT N#	DESCRIPTION			CODE N#
		TYPE	WIDTH	THICKNESS	
1921	47-47-4	Grading	24'		
	(1)				
1922	47-47-4	Gravel	24'	2"	
					Maint. Dept.
1932	47-47-21-2	Grading Gravel	40' 32'	1"	
	(1)				600 C.Y./Mile.
1935	47-47-21-2	Oil Tr. Gravel	24'	1"	
					136.05 Gal./Mile Maint. Dept.
1937	47-47-21-2C	Concrete	20'	9-7-9	
M	1940	A.F.E. 27			
		Bit. Retreat			MC-3-3083 Gal./Mi. Grav. 132 C.Y./Mi. Maint. Dept.
M	1941	A.F.E. 37			
		Bit. Retreat	28'		SG-4-5375 Gal./Mi. Grav. 188 C.Y./Mi. Maint. Dept.
M	1944	A.F.E. 4			
		Spot Treat. Bit. Surf. Repair			MG-3-2540 Gal./Mi. Grav. 86 C.Y./Mi. Maint. Div.
C	1946	5101-01			
	(2)	Regrading Concrete Mono. Curb, E. Ext.	20'	9-7-9	C64, W66, W100, C1010.
C	1976	5101-05			
		WIDENING Asph. Conc. Surf. Cura & Gutters	42'	2 1/4"	
M	1973	SF			
		Agg. Shoulders	10'	Var.	
C	1982	5101-08			
		Bit. Widening Bit. Surfacing Agg. Shoulders	25' 6" 28' 4" 6'	6" 4" Var.	R1 Turn Ln, CSAH-25
M	1988	4317			
		Bit. Sealing			
C	1999	5101-13			
		Bit. Overlay Gravel Surface	28' 1 1/2" 6' 2 1/2"		Spec 2350 Class 1

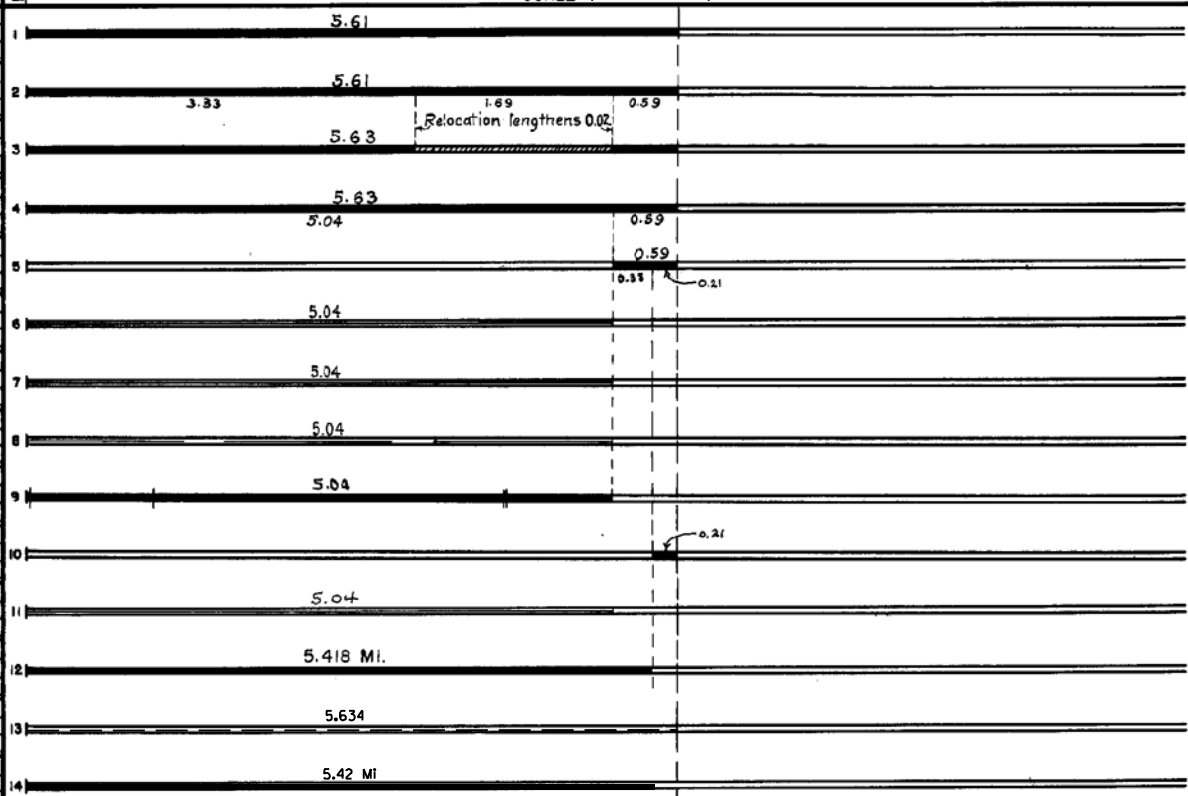

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1931	5.61	5.02	0.00	0.39	0.00	5.61	0.00	0.00	0.00
1932		5.63	5.04	0.00	0.59	0.00	5.63	0.00	0.00	0.00

REMARKS: Layout is to Scale as of 1932.

(1) This work not done under these project numbers but lies within the limits of these projects.

(2) Contract not final but work substantially complete in 1946.

