


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 6009  
TRUNK HIGHWAY 59  
COUNTY Polk  
DISTRICT 2B

LIMITS: Jct. T.H. 2 - N. Co. Line

Ref. Pt. 323+00.479 - 330+00.643



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° Dist
		TYPE	WIDTH	THICKNESS	
		Gravel	26' 3"	3"	No Record of Constr.
					Added in 1934.
1931		Gravel	26'	2"	Co. Job 8103. Added in 1934. 1000 C.Y./Mi. 37' L.L.
M	1942 A.F.E. 6	Regraveling			260 C.Y./Mile. Maint. Dept.
M	1943 A.F.E. 6	Grav. Resurface (Spots)			684 Gal./Mi. Maint. Dept.
C	1947 6009-01	Grading & Stab. Gravel	42'	9"	1200 C.Y./Mi. 846
C	6009-03	Br. 6449	30'		40' C.D.G. 847
C	1949 6009-06	Stab. Gravel Base	36'	3"-12"	
		Mixed Bit.	26'	1"	1349
M	1951 A.F.E. 4	Bit. Fog Seal	26'		RCS-1, 10415 Gal. Agg. 280 C.Y.
C	1955 6009-07	Bit. Stab. Base	40'	0'-9"	added thickness
	A.F.E. 821	Plant Mix Bit. Guard Rail	24'	3'-4"	At Br. 6449 2055
M	1956 A.F.E. 605	Heavy Bit. Seal	24'		RC-5, 21266 Gal. Agg. 910 C.Y.
M	1965 C	Light Bit. seal	25'		RS-10, 12490 Gal. Agg. 490 C.Y.
C	1969 6009-09	Pl. Mix Bit. Surf. Gravel Shoulders	24'	1 1/2"	2469
C	1974 6004-05	Grade Base Surface	24'	3'	1470
	F008-1(45)	Pl. Mix Bit. SHLDERS	12'		671
C	1971 6009-10	PLATE BEAM GUARD RAIL			500 LIN. FT. 471
M	1983 6009-11	Bit. Surfacing	24'	2"	Sp 2331
	F022-4(41)	Bit. Surfacing	30'	1 1/2"	Sp 2341
		Agg. Shoulders	4'	Var	Sp 2221

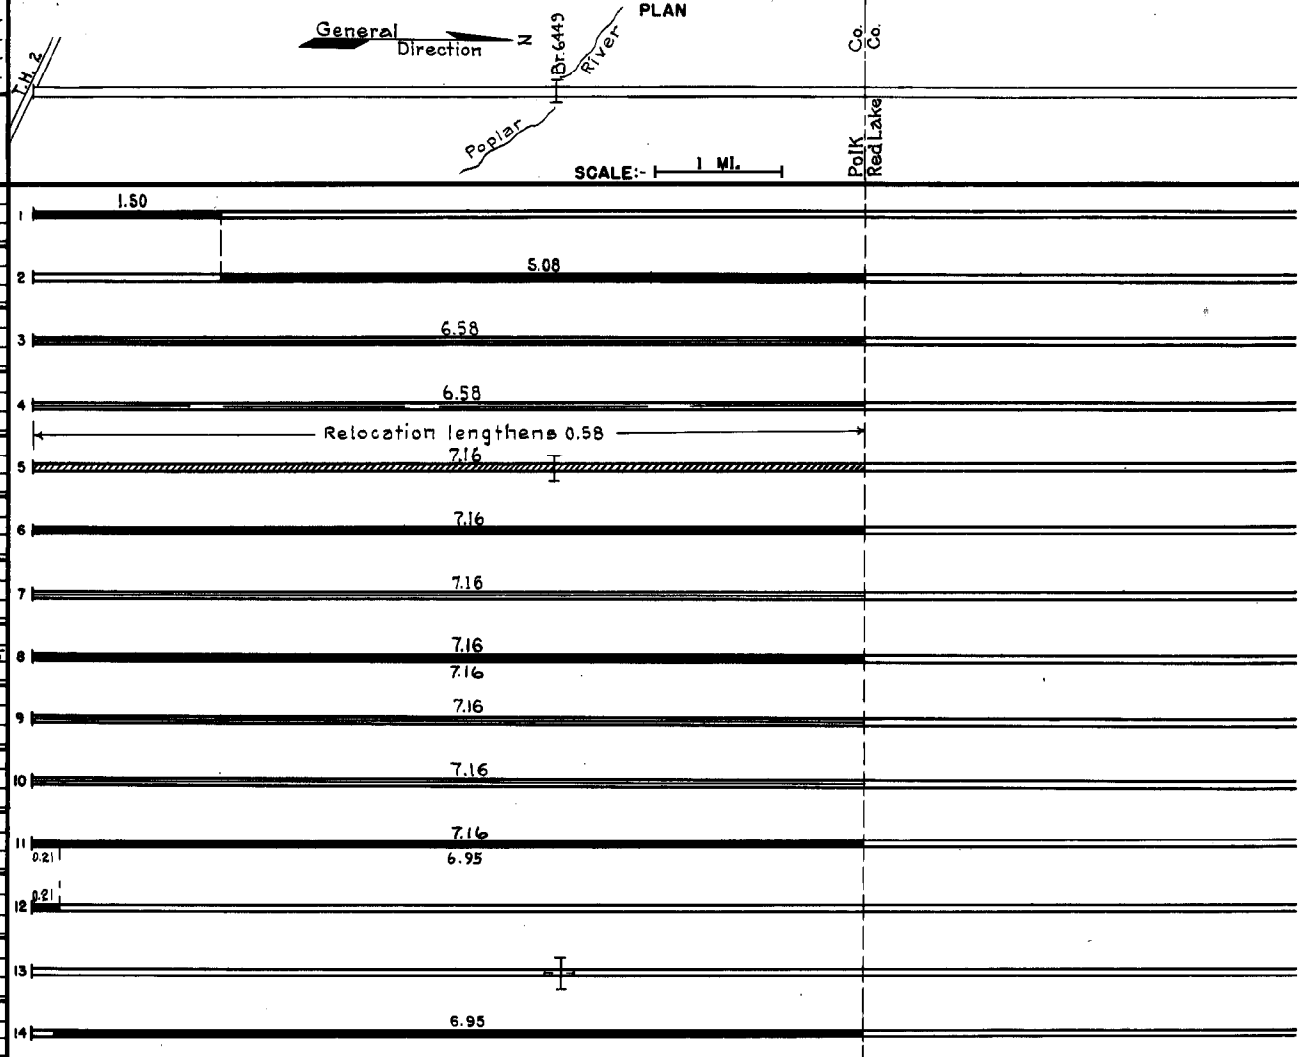

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1946	6.58	6.27	0.01	0.30	0.00	6.57	0.01	0.00	0.00
1947		7.16	7.15	0.01	0.00	0.00	7.15	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1934  
FOR OTHER PROJECTS SEE DIST. No. 1270

