


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6304
TRUNK HIGHWAY 92
COUNTY Red Lake
DISTRICT 28

LIMITS: Jct. T.H. 32 - Jct. T.H. 59 (In Brooks)



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o Dist	T.H.
		TYPE	WIDTH	THICKNESS		
1922	92-65-2	Grading Gravel 5 Bridges (1)	24	3 1/2"	1600 C.Y./Mi.	1
1922	92-65-02A	Grading Gravel Br. 3740 & 3515	24	3 1/2"	Co. Job. 2201 1600 C.Y./Mi. 2-30' C.D.G.	2
1932	92-65-2 (2) 92-65-02(2)	Oil Treated Grav.	24	1 1/2"	12963 Gal./Mi. Maint. Dept.	3
M	A.F.E. 24	Bit. Retreat			SC3, 6773 Gal./Mi. Grav. 111 C.Y./Mi. Maint. Dept.	4
M	A.F.E. 21	Bit. Seal Coat (High Type)	24		RC3, 3274 Gal./Mi. Agg. 88 C.Y./Mi. Maint. Dept.	5
C	A.F.E. 20	Grade Lift Mixed Bit.	28	6"		6
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24		SC&RT, 444 Gal./Mi. Grav. 14 C.Y./Mi. Maint. Dept.	7
M	A.F.E. 4	Bit. Seal Coat (Spots)	22		MC3, 722 Gal./Mi. Grav. 18 C.Y./Mi. Maint. Div.	8
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24		SC3, 1145 Gal./Mi. Grav. 60 C.Y./Mi. Maint. Div.	9
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24		SC3, 12270 Gal. Agg. 629 C.Y.	10
		Oil Tr. Gravel	24	1 1/2"	Transferred from C.S. 6305 in 1947. See C.S. 6305 for history.	11
M	A.F.E. 4	Bit. Fog Seal (Spots)	24		SC3 & RT, 4,906 Gal. Agg. 175 C.Y.	12
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair			SC3, 13754 Gal. Agg. 812 C.Y.	13
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair			SC3, 9700 Gal. Agg. 608 C.Y.	14

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1922	1946	13.67	13.62	0.05	0.00	0.00	13.62	0.05	0.00	0.00
1947	1952	14.14	14.09	0.05	0.00	0.00	14.09	0.05	0.00	0.00
1953	1954	12.98	12.97	0.01	0.00	0.00	12.97	0.01	0.00	0.00
1955		12.98	12.24	0.01	0.73	0.00	12.97	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1922.
 (1) Br. 1917, 69' B.S.; Br. 3406, 52' C.D.G.; Br. 3404, 52' C.D.G.; Br. 1742, 18' B.S. & Br. 2012, 30' B.S.
 (2) This work not done under these project numbers but lies within the limits of these projects.

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6304
TRUNK HIGHWAY 92
COUNTY Red Lake
DISTRICT 2B

LIMITS: Jct. T.H. 32 - Jct. T.H. 59 (In Brooks)

Ref. Pt. 000+00.000 - 012+00.992

YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° Dist
		TYPE	WIDTH	THICKNESS	
C	6304-02	Grading Gravel & Salv. Bit. Culverts (3)	28'	2"	10 Sand Mat'l 1200 C.Y./Mi. 1553
C	6304-03	Br. 6830	30'		3-24' C.S. 1653
C	6304-04	Sand-Grav. Sub-base Gravel Base Plant Mix Bit. A.F.E. 821*	30' 30' 24'	0'-9" 3'-4" 1 1/2"	A.F.E. 821 covers guard rail at Br. 6829 & Br. 6819 2254
C	6304-05	Xing Signals			
M	C	Light Bit. Seal	25'		CRS-1, 28666 Gal. FA-1, Agg. 823 C.Y. 367
C	6304-06	Bit. SURFACING TURN LANES AGG. SHOULDERS	24' 3'	3"	2076
C	6300-01	PLATE BEAM GUARD RAIL AT Br. 6830			375 LIN. FT. 1774
C	6300-02	GUARD RAIL AT BR. # 6829, 8834, 8835, 8819, & 8836.			1912 LIN. FT. 378
M	SF	Agg. Shoulder Repair	3	1 1/2"	2700 Tons
S	6304-08	Bit Overlay	24'	2"	Spec 2360 12.992 Mi
M	8822-30	Bit. Seal Coat	24'		Spec. 2356 12.973 Mi

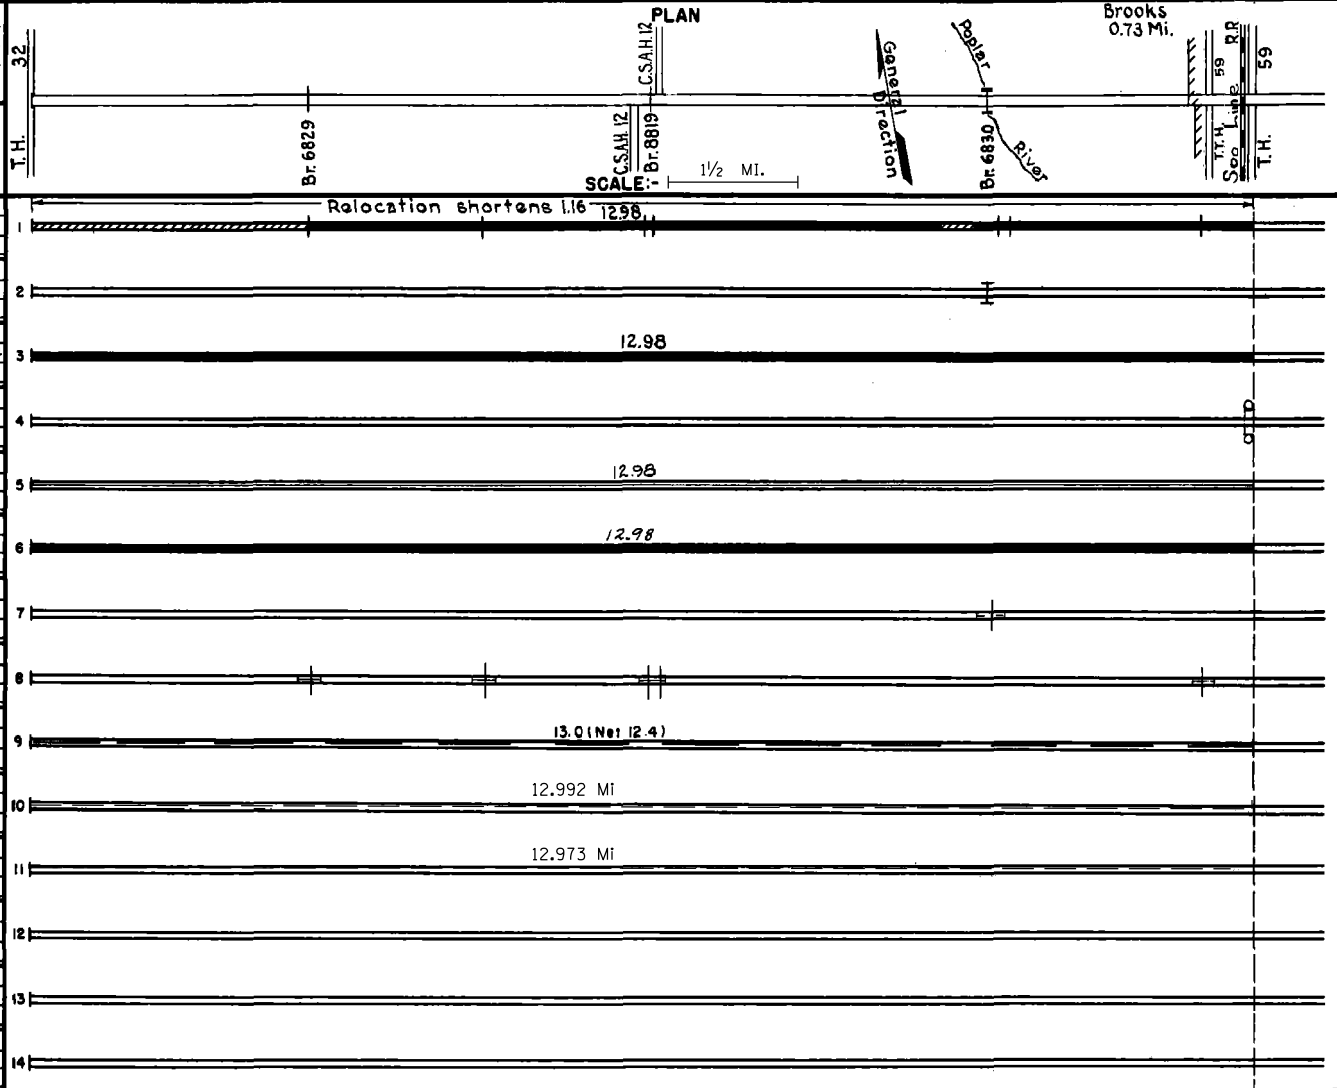

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1
(3) C(11-14-11) 12T(Br. 6829), C108, C128, C1212 D(Br. 8819), Ext W66 & W88, & C1010 H
