


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 6402
TRUNK HIGHWAY 19
COUNTY Redwood
DISTRICT 8B

LIMITS: W. Co. Line - N. Co. Line (Jct T.H. 67)

Ref. Pt. 044+00.614 - 057+00.360



YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel	20'	2"	No Record of Constr.	
	19-14-11	Concrete Spillway				
1920	19-14-7	Grading (1) Gravel	20' 20'	3"	Co. Job 1906 1200 C.Y./Mile.	
1931	19-14-25-2A & B	Grading Br. 5101	40' 27'		120' L.T.	
1931	19-14-25-2A	Concrete	20'	9-7-9		
1931	19-14-25-2B	Gravel	32'	1/4"	800 C.Y./Mile.	
1932	19-14-25-2B	Concrete	20'	9-7-9		
C	1956 6402-01 6402-02	Rdwy. Drainage			Install C.M. Culvs.	
C	1966 Maint. Proj.	Plant Mix Bit Gravel Shoulders	20'	3"	Over P.C. Conc. Imp.	
C	1973 6402-08	Remove Lip Curb Agg. Shldr's		8"		
M	1973 SF	Crack + Joint Seal			50,000 Lin. Ft.	
C	1982 6402-13	Bit. Surfacing Agg. Shoulders	30'	2 1/2" 5' Var.		
C	1983 6402-13	Bit. Widening Bit. Surfacing	25'	8 1/2" 4"	Li. & Rt.	
C	F-PMS 014-11431	Agg. Shoulders	5'	Var.		
C	1988 6402-16	Grading Bit. Surfacing	28'	5 1/2" 1"	Spec. 2331 Spec. 2341	

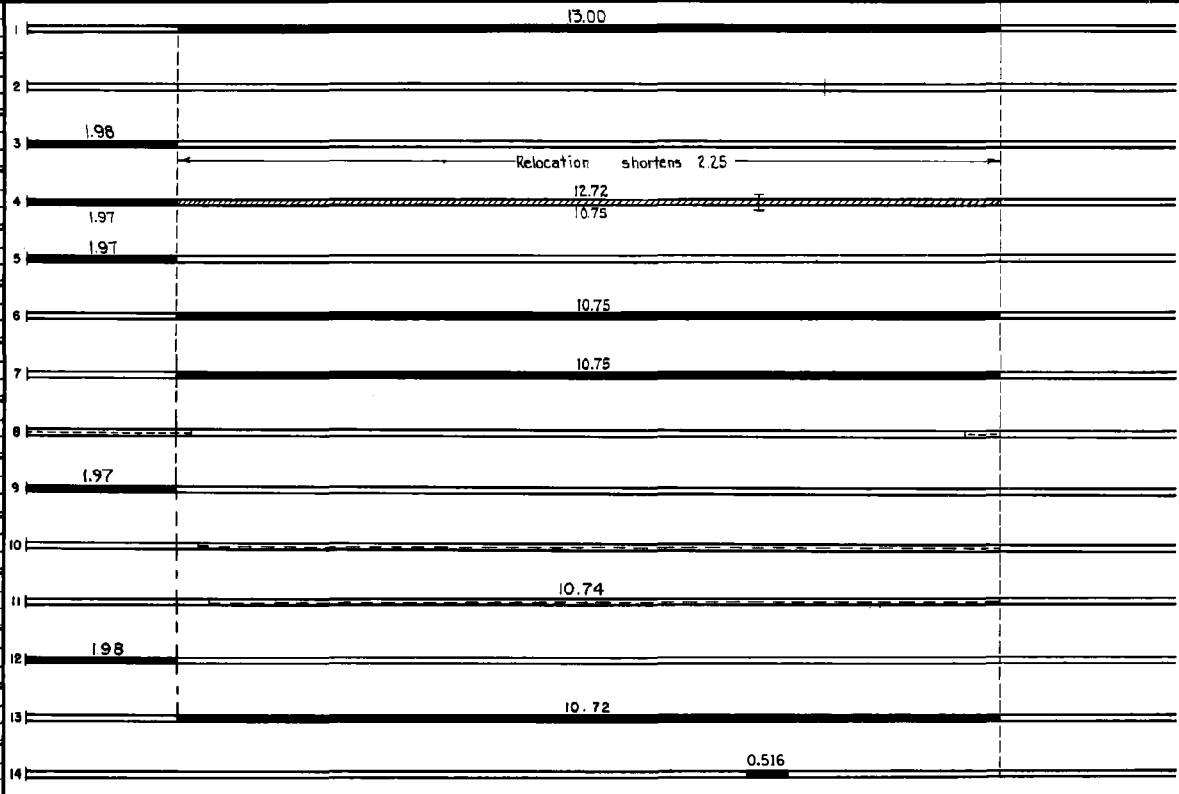

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1930	14.98	5.73	0.00	2.5	0.00	14.98	0.00	0.00	0.00
1931		12.72	11.68	0.02	1.02	0.00	12.70	0.02	0.00	0.00

REMARKS: Layout is to scale as of 1931.
(1) No record of construction of grading.

