


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6512
TRUNK HIGHWAY 212
COUNTY Benville
DISTRICT 8A

LIMITS: Jct. TH.4 in Hector - E. Co. Line
Ref. Pt. 090+00.943 - 101+00.807



YEAR BUILT	PROJECT N°	DESCRIPTION			REMARKS	CODE N°
		TYPE	WIDTH	THICKNESS		
		Gravel	20'	3"	No Record of Constr.	
1919	212-12-10	Grading	26'		Co. Job 1902.	
1920	212-12-9	Gravel	20'	2"	Co. Job 2004.	
1929	212-12-34-3	Grading	40'			
1930	212-12-34-2	Br. 6299 Grading Gravel	40' 32'	1 1/2"	WY1010DY 84. 1000 C.Y. / Mile.	
1930	212-12-34-3	Gravel	38'	1 1/2"	1000 C.Y. / Mile.	
1931	212-12-34-2E3	Concrete	20'	9" x 9"		
M	1949 A.F.E. 34	Gravel Shoulders (Spots)			1232 C.Y.	
M	1951 A.F.E. 27	Regravel Shoulders (Spots)			1976 C.Y.	
C	1959 6512-01	Base Widening * Plant Mix Bit. Bit. Shoulders	24'	3"	*Rdwy. imp. widened with sub-base and Bit. Stab. Base	
M	1966 C	Light Bit Seal	25'		CRS-1, 234.14 Gal. Agg. 648 C.Y.	
M	1971 6512-03	Pl. Mix Bit. Seal	24'	3/4"		
C	1982 6215-05 (F-PMA-012-1137)	Remove Old Bituminous and Resurface	24'	4 3/4"		
C	1992 6512-06	Bit. Overlay	24'	1 1/2"	Spec. 2341	

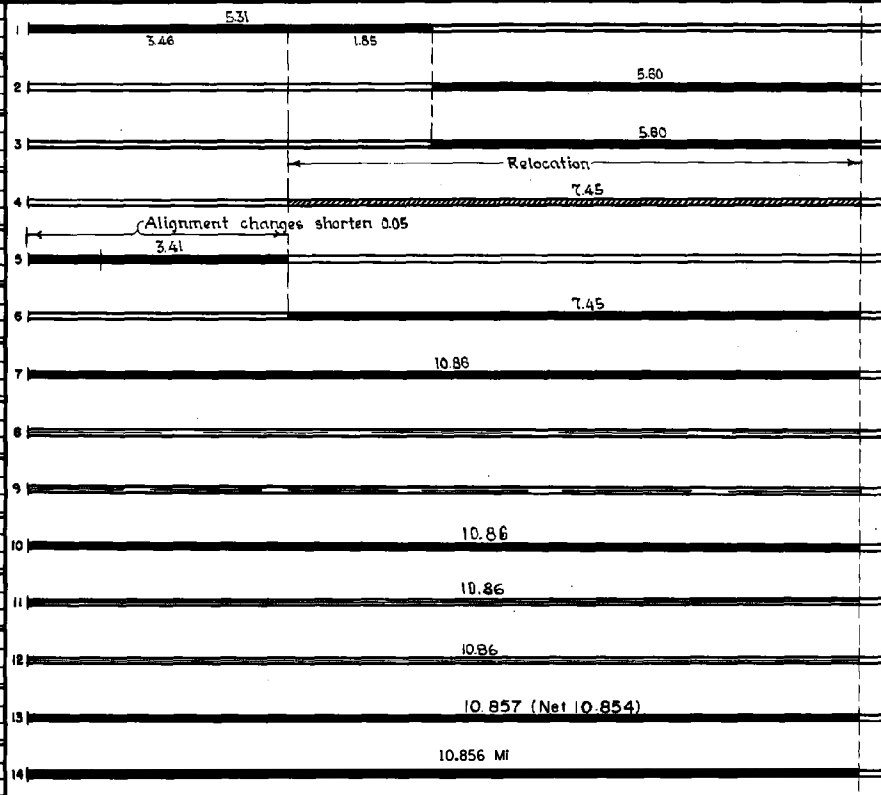

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1928	10.91	9.37	0.00	1.54	0.00	10.18	0.00	0.73	0.00
1929	1929	10.91	9.39	0.00	1.52	0.00	10.18	0.00	0.73	0.00
1930		10.86	9.37	0.00	1.49	0.00	10.16	0.00	0.70	0.00

REMARKS: Layout is to scale as of 1930.

