


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6605  
TRUNK HIGHWAY 21  
COUNTY Rice  
DISTRICT 7A-6B

LIMITS: W.Co.Line - Jct.C.S.A.H.46



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Gravel	22'	2"	No Record of Constr.
		Gravel	28'		No Record of Constr.
1919	21-21-5	Grading	26'		Co. Job 1901.
1920	21-21-2	Gravel	26'	3"	Co. Job 2006. 1200 C.Y./Mile.
1921	21-24-4	Grading	24'		
		Gravel	20'	3"	1200 C.Y./Mile.
1932		Oil Tr. Gravel	26'		7000 Gal./Mile. Maint. Dept.
1937	21-21-26-2A	Grading	32'		
		Br. 5658	36'		B.S. U.P.
1938	A.F.E. 28	Mixed Bitum.	26'	1"	
					Maint. Dept.
M	1940	A.F.E. 24			Bit. 3736 Gal./Mi. Grav. 256 C.Y./Mi. Maint. Dept.
M	1940	A.F.E. 35			Spot Graveling 134 C.Y./Mi. Maint. Dept.
M	1941	A.F.E. 17			Bit. Retreat. 5C3, 6050 Gal./Mi. Maint. Dept.
C	6605-07				C66X82, C46X38, W33 Ext to 84; & 2-C46X36.
1941	6605-08	5 Culverts			
C	6605-01	Grading	34'		
1942	6605-02	Gravel			1200 C.Y./Mi.
C	1942	A.F.E. 19			Seed supplied by R.S.D. (S.P. 6605-11)
		A.F.E. 7			Guard Rail Seeding Maint. Dept.

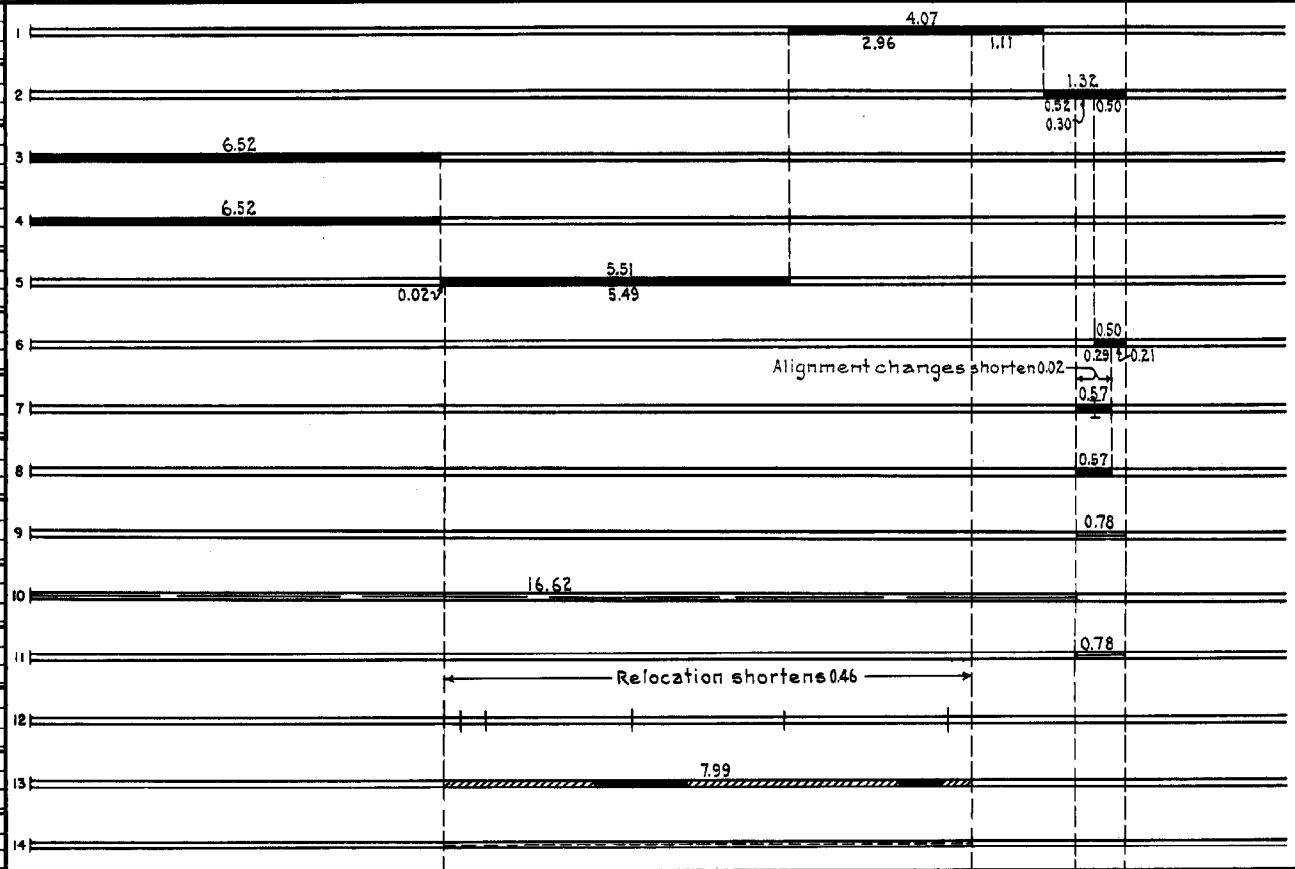

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921	1936	17.42	16.10	0.00	1.32	0.00	16.10	0.00	1.32	0.00
1937	1941	7.40	16.10	0.00	1.30	0.00	16.10	0.00	1.30	0.00
1942	1946	16.94	15.64	0.00	1.30	0.00	15.64	0.00	1.30	0.00
1947	1952	16.60	15.30	0.00	1.30	0.00	15.30	0.00	1.30	0.00
1953		14.70	14.70	0.00	0.00	0.00	14.70	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1937







