

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6948
TRUNK HIGHWAY 73
COUNTY St. Louis
DISTRICT 1B


LIMITS: (In Hibbing) E. Jct. T.H. 169 - N. Jct. T.H. 169

Ref. Pt. 079+00.637 - 082+00.511

Hibbing
3.00 Mi.

PLAN

YEAR BUILT	PROJECT N ^o	DESCRIPTION		REMARKS	CODE N ^o
		TYPE	WIDTH THICKNESS		
C	1956 6948-01	Grading Grav. Base & Sub-base Mixed Bit. (Base)	80' 15" 52' 1 1/2"	Divided Highway Const. C1010H+45°	
C	1958 6948-04	Concrete	48' 8"		
C	1959 6949-05	Traffic Signals A.F.E. 605		8022 Gal. MC-2, Agg. 120 CY.	
C	1961 & 1964 6949-06	Lighting Systems Frontage Road			
C	1964 6949-07	Grading, Base, Bit.	24' 1 1/2" 24'	By Maint On Frontage Road	
M	1969 SF	Left Turn Lanes	14' 1"	Jct. of 23rd St.	
M	1970 SF	Shoulder Resurface	6-18 Var.	MC250 Tack 935 Gal. Agg 923 Tons	
C	1934 69-35-34-1890	Concrete	20' 9-9"		
C	1955 6934-25	Hot Asphaltic Conc.	22' 3"	on old Conc. Base	
C	1947 6934-14	Traffic Signals	56'		
C	1947 6934-14	Asphaltic Conc.	40' 2 1/2" 56'	on old P.C. & Bit. Conc. Base	
C	1947 6934-14	Bit. Stab. Gravel Plant Mix Bit.	26' 6" 22' 1 1/2"		
C	1974 6984-64	Grading Bit. Surface	56' 5"		
C	1979 6949-16	Asph. Cement Bit. Resurfacing	24' 34" 56'	356 Ton AC SPG 2361 4448 Ton	
C	1980 6948-15	Traffic Control System & Signal		On T.H. 169 27th St.	

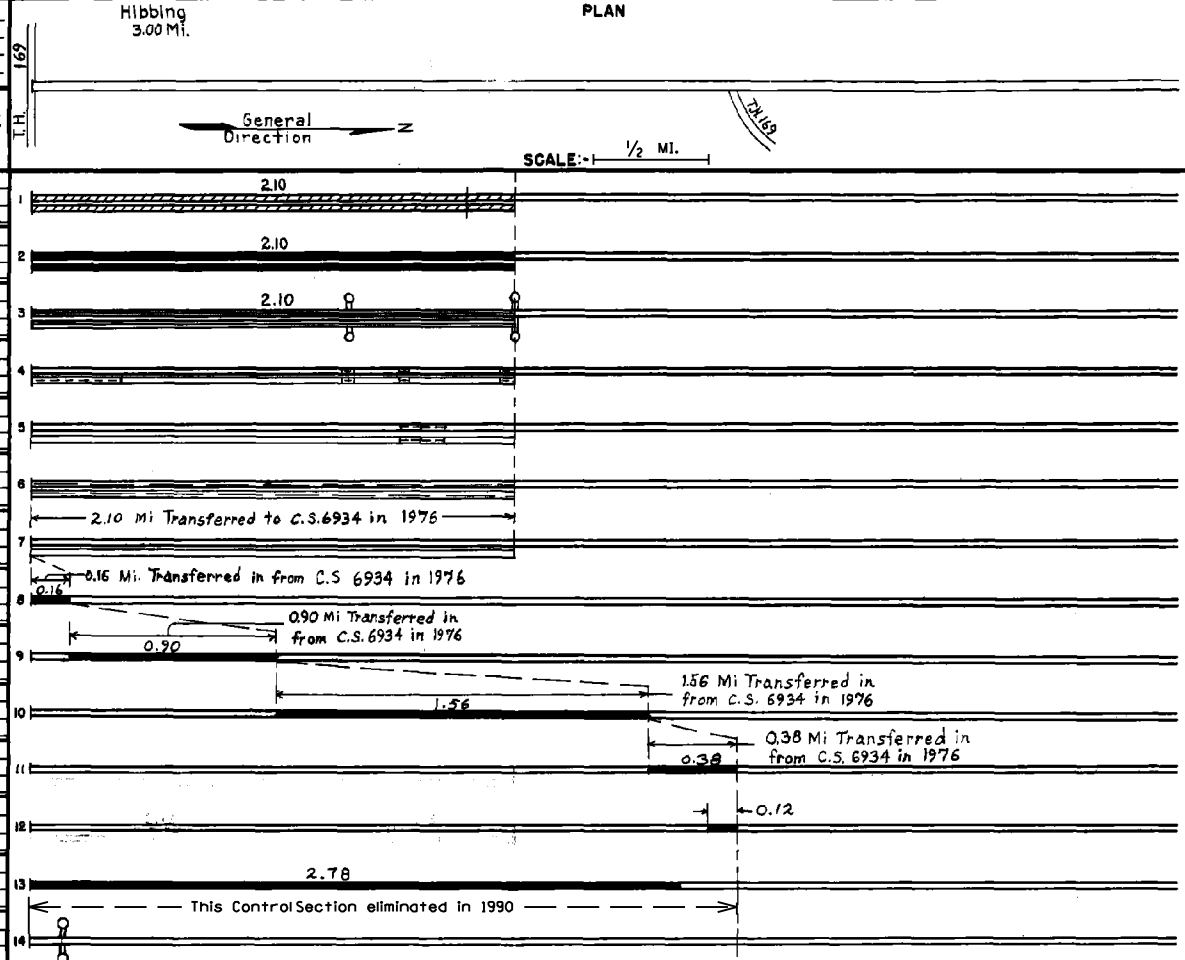

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1956	1975	2.10	0.00	0.00	2.10	0.00	0.00	0.00	2.10	0.00
1976		3.00			3.00				3.00	

REMARKS: Layout is to scale as of 1956
