


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7212  
TRUNK HIGHWAY 93  
COUNTY St. Louis  
DISTRICT 7A

LIMITS: Jct. T.H. 169 - Jct. T.H. 19 in Henderson  
Ref. Pt. 001+00.700 - 005+00.600



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1946	72-501-04	Stab. Grav. Base & Var. Mixed Bit. Br. 6951 & 3355	24'	1 1/2"	Added in 1949 W105D & 94 L.T.
M	A.F.E. 4	Bit. Surf. Repair	24'		MC313C3, 1808 Gal. Agg. 100 C.Y.
M	A.F.E. 819	Spot Stab. Grav. Lifts			5C3, 18851 Gal. Agg. 794 C.Y.
1953	A.F.E. 604	Spot Treat. Bit. Surf. Repair			
M	A.F.E. 604	Spot Treat. Bit. Surf. Repair	24'		MC3, 11628 Gal. Agg. 759 Tons
M	A.F.E. 605	Light Bit. Seal	24'		RC2, 9464 Gal. Agg. 317 C.Y.
M	1960	Spot Treat. Bit. Surf. Repair	24'		MC3, 4222 Gal. Agg. 277 Tons
C	1961	Grading Gravel & Bit. Base Road Mix Bit.	24'	1 1/2"	
C&M	1962	Plant Mix Bit. Spot Treat. Bit. Surf. Repair	24'	2"	Plant Mix 49 Tons
M	1963	Spot Treat. Bit. Surf. Repair	24'		Plant Mix 108 Tons MC-3 Tack 200 Gal.
C	1968	Pi. Mix Bit. Surf. Gravel Shldr.	24'	2 1/2"	Bit. Mat'l. 355 Ton
M	1975	Gravel Shldr.	2'	1-3"	414 Tons 3/4" Agg.
C	1984	Grading, Agg. Shoulders. Pi. Mix Bit. Surfacing. Br. 72005 Repl. Br. 3355	11.5'	3 1/2"	Sp. 2221 1166 Tons Sp. 2341 420 Tons Contract No. 18832
M	1985	Bit. Surfacing. Agg. Shoulders	24'	2"	Sp. 2341 Sp. 2221
M	1998	Bit. Overlay. Agg. Base (Shoulders)	24'	2"	Spec. 2350 Class 5

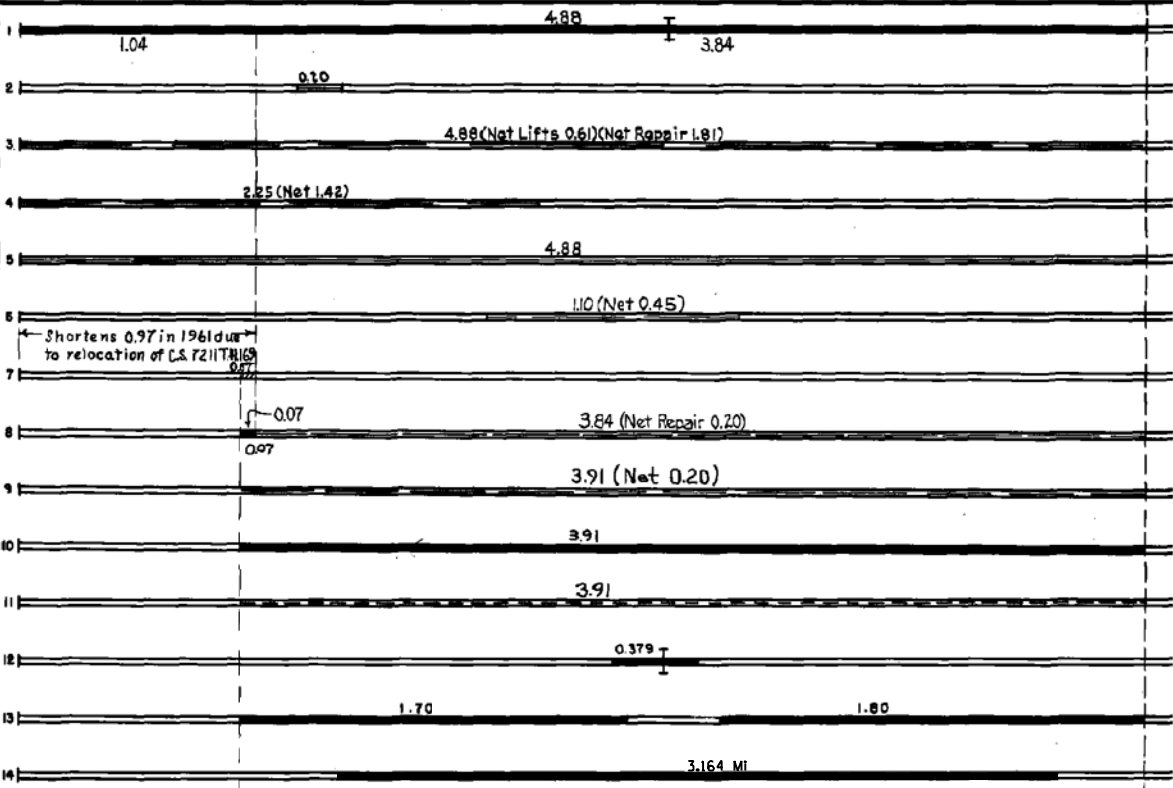

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1949	1960	4.88	4.40	0.07	0.42	0.00	4.88	0.00	0.00	0.00
1961	1973	3.91	3.43	0.02	0.46	0.00	3.89	0.02	0.00	0.00
1974		3.91	3.40	0.02	0.49		3.89	0.02		

REMARKS: Layout is to scale as of 1949

