


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0806  
TRUNK HIGHWAY 68  
COUNTY Brown  
DISTRICT 7B

LIMITS: Jct. T.H.15 - East County Line



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
1930		Gravel	24'	2 1/2"	Co. Job N° 2902. 1200 C.Y./Mile. Added in 1934.
1935	83-83-21	Grading Br. N° 5431	32'	30"	132' C.D.G. - 0H.
1936	83-83-21	CaCl <sub>2</sub> Stab Grav. Sand Base	24'	2" 10"	13" Sand sub. base. 1" Sand stab. base.
1937	83-83-21 A.F.E. 20-Dist. 14	Oil Tr. Gravel	24'	1 1/2"	15408 Gal./Mile. Maint. Dept.
1937	A.F.E. 10	Seeding			Maint. Dept.
M	A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		MG 3,2099 Gal./Mi. Grav. 104 C.Y./Mi. Maint. Div.
C	A.F.E. 16	Bit. Resurfacing Mixed Bit.	24'	7/8" added	MG 2,9629 Gal./Mi. Grav. 415 C.Y./Mi. Maint. Div.
M	A.F.E. 5	Bit. Seal Coat	26'		RC 4, 17574 Gal. Agg. 400 c.y.
M	A.F.E. 604 A.F.E. 605	Bit. Surf. Repair Light Bit. Seal	24'		SC 36RS 2, 3448 Gal. Agg. 45 Tons & 118 C.Y.
C	0806-05	Sand Grav. Subbase Bit. Stab. base Plant Mix Bit.	34'	6" 4" 1 1/2"	Grad. or Shoulder Grad.
M	1957 A.F.E. 605	Bit. Seal Coat	25'		RS-2, 11410 Gal. Agg. 405 C.Y.
M	1964 C	Light Bit. seal	25'		RS-2K, 5878 Gal. Agg. 200 c.y.
M	1966 SF	Bit. Surf. Repair	24'	1 1/2"	RC-2 Bit, 170 Gal. Pl. Mix Bit, 1639 Ton
C	1969 0805-22	Grade, Base Pl. Mix. Bit. Surf. Pl. Mix. Bit. Shldr.	24'	3"	

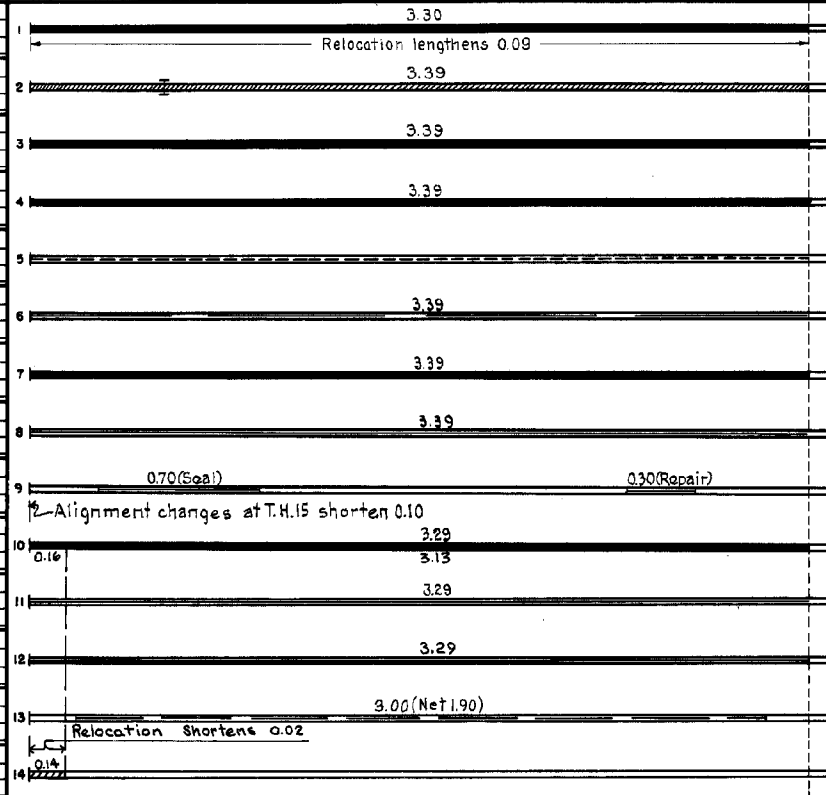

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.		RDWY. MI.	BR. MI.		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1934	3.30	3.30	0.00	0.00	0.00	0.00	3.30	0.00	0.00	0.00	
1935	1955	3.39	3.36	0.03	0.00	0.00	0.00	3.36	0.03	0.00	0.00	
1956	1966	3.29	3.26	0.03	0.00	0.00	0.00	3.26	0.03	0.00	0.00	
1969		3.27	3.24	0.03	0.00	0.00	0.00	3.24	0.03	0.00	0.00	

REMARKS: Layout is to scale as of 1935

(1) This work not done under this project number but lies within the limits of this project.

