

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 6306  
TRUNK HIGHWAY 222  
COUNTY Red Lake  
DISTRICT 2B

LIMITS: Jct. T.H. 92 - 1st Ave. in Oklee

Ref. Pt. 000+00.000 - 001+00.474

General Direction → z  
PLAN Oklee 0.47 Mi.

YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION				CODE N <sup>o</sup> DIST.
		TYPE	WIDTH	THICK-NESS	REMARKS	
1941	63-503-01	Grading Gravel	32'	4"	Added in 1949	
C	1949 A.F.E. 28	Bit. Surfacing Bit. Surf. Treat.	24'	3/4"	503.9506 Gal.	
C	1951 A.F.E. 21	Sand-Grav. Base Bit. Surfacing Mixed Bit.	30'	7 1/2"	MC-3, 24023 Gal. Agg. 984 C.Y.	
C	1953 6306-01	Gravel Base Plant Mix Bit.	28'	6"	added thickness	1353
C	1962	Gravel Shouldering			Gravel, 2987 Tons 3 Rt. & Lt.	1362
M	1970 6305-05	RECONSTRUCT JCT. REMOVE Y, CONST TURN LANE				1370
C	1970 6306-03 S.E.	Bit. Recurl Gravel Shoulders	24'	3"	Pl. Mixed Bit. Spec. 2361 1.18 Agg. Shouldering	1189
S	2003 6306-04	Bit. Overlay	26'	1 1/2"	Spec. 2360	
	2012 8822-136	Bit. Seal Coat	26'			

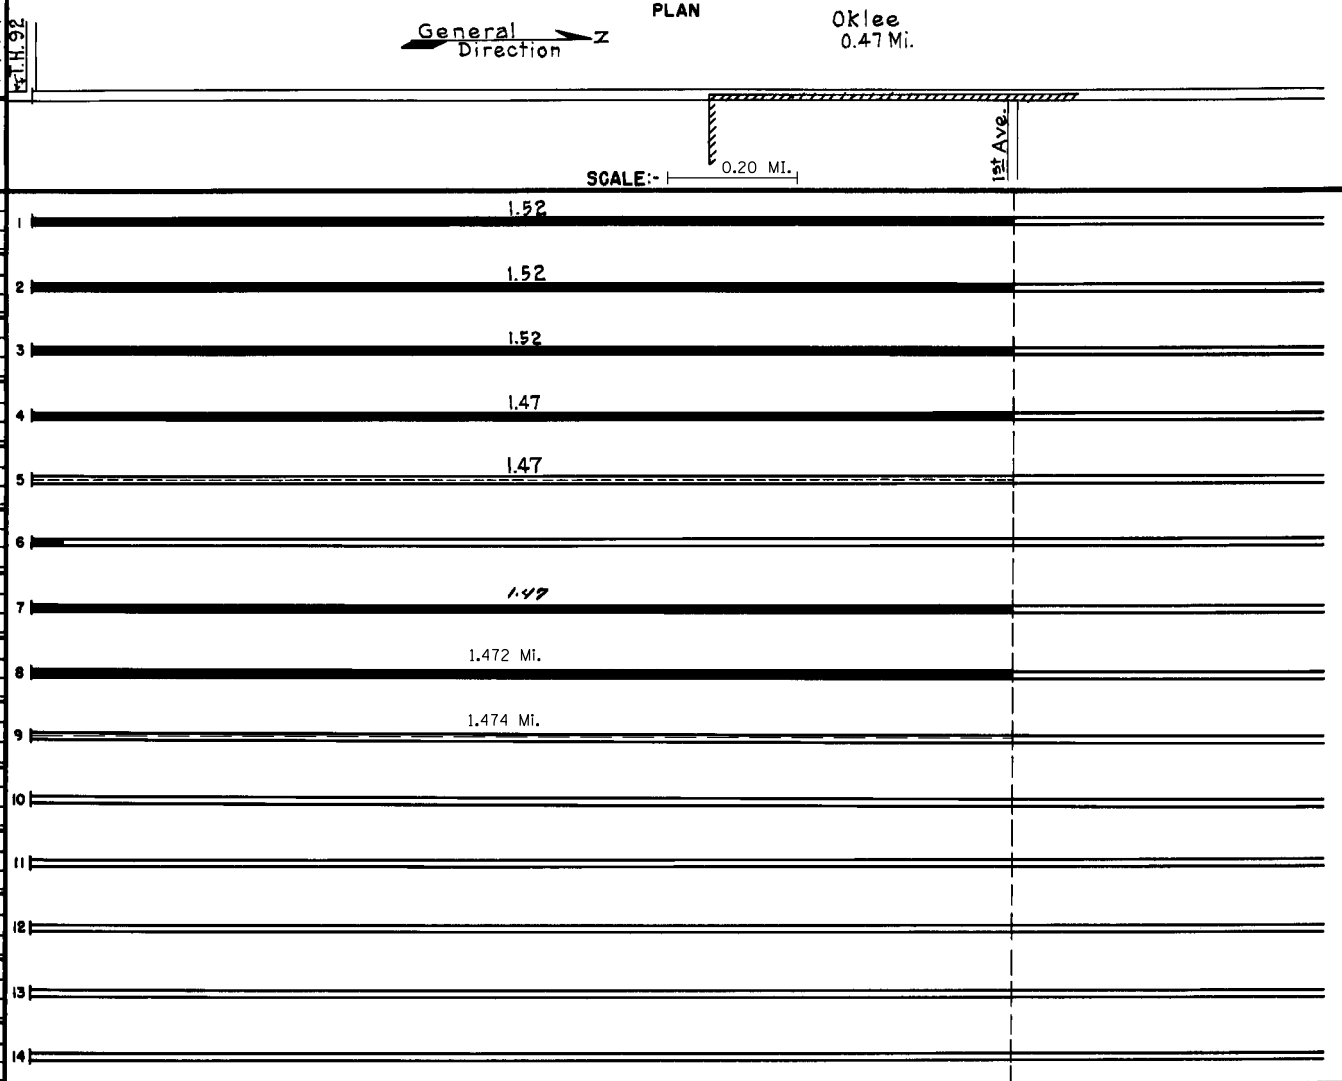

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1952	1.52	1.05	0.00	0.47	0.00	1.52	0.00	0.00	0.00
1953		1.47	1.00	0.00	0.47	0.00	1.47	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1949
