FORM R.L.-7 REV. 7-70

SHEET 1 OF 1

PREPARED BY
TRANSPORTATION & TRANSIT PLANNING & PROGRAMMING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0282
TRUNK HIGHWAY 35E
COUNTY Anoka
DISTRICT Metro

LIMITS: Ramsey - Anoka Co. Line - N. Jct. T.H. 35 & 35 W

Ref. Pt. 120+00.382 - 127+00.420

YEAR BUILT	PROJECT No.	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C 1970	6281-03	Grading			Divided Highway
	6281-04	Gravel Base		6"	
		P.C. Concrete	2@24'	8"	Pl. Mix Bit. Shoulder
C 1970	0282-06	Grading			Divided Highway
		Br. 02802			210' P.P.G. - U.P.
		Br. 02803			209' B.S. - U.P.
C 1970	0282-09	Gravel Base		6"	
		P.C. Concrete	2@24'	8"	
		Pl. Mix Bit. Shoulders			
C 1970	0283-03	Grading			Divided Highway
	0283-07	Gravel Base		5"	
		P.C. Concrete	2@24'	8"	
C 1971	0282-14	Lighting			CSAH 14
C 1994	0282-24	Bit. Overlay	24'	1"-½"	61WEA75100X-Spec. 2340
		Br. 02802, Br. 02803		1"-½"	61BIB75100X-Spec. 2340
M 1995	0282-95036	Major Crack Repair			
M 2001	8825-102	Rout & Seal			Spec. 3725
S 2011	0282-34	Grading			
		Bit. Mill & Surfacing	24'	2"	
		Conc. Overlay	24'	9"	Unbonded
2013	0282-36	Transverse Grooves			RT Lane
2016	0282-39	Grading/ Agg. base	var.	var.	Class 6
		Bit. Surfacing	var.	7"	Spec. 2360
	(6282-47)	Conc. Surfacing	var.	9"	

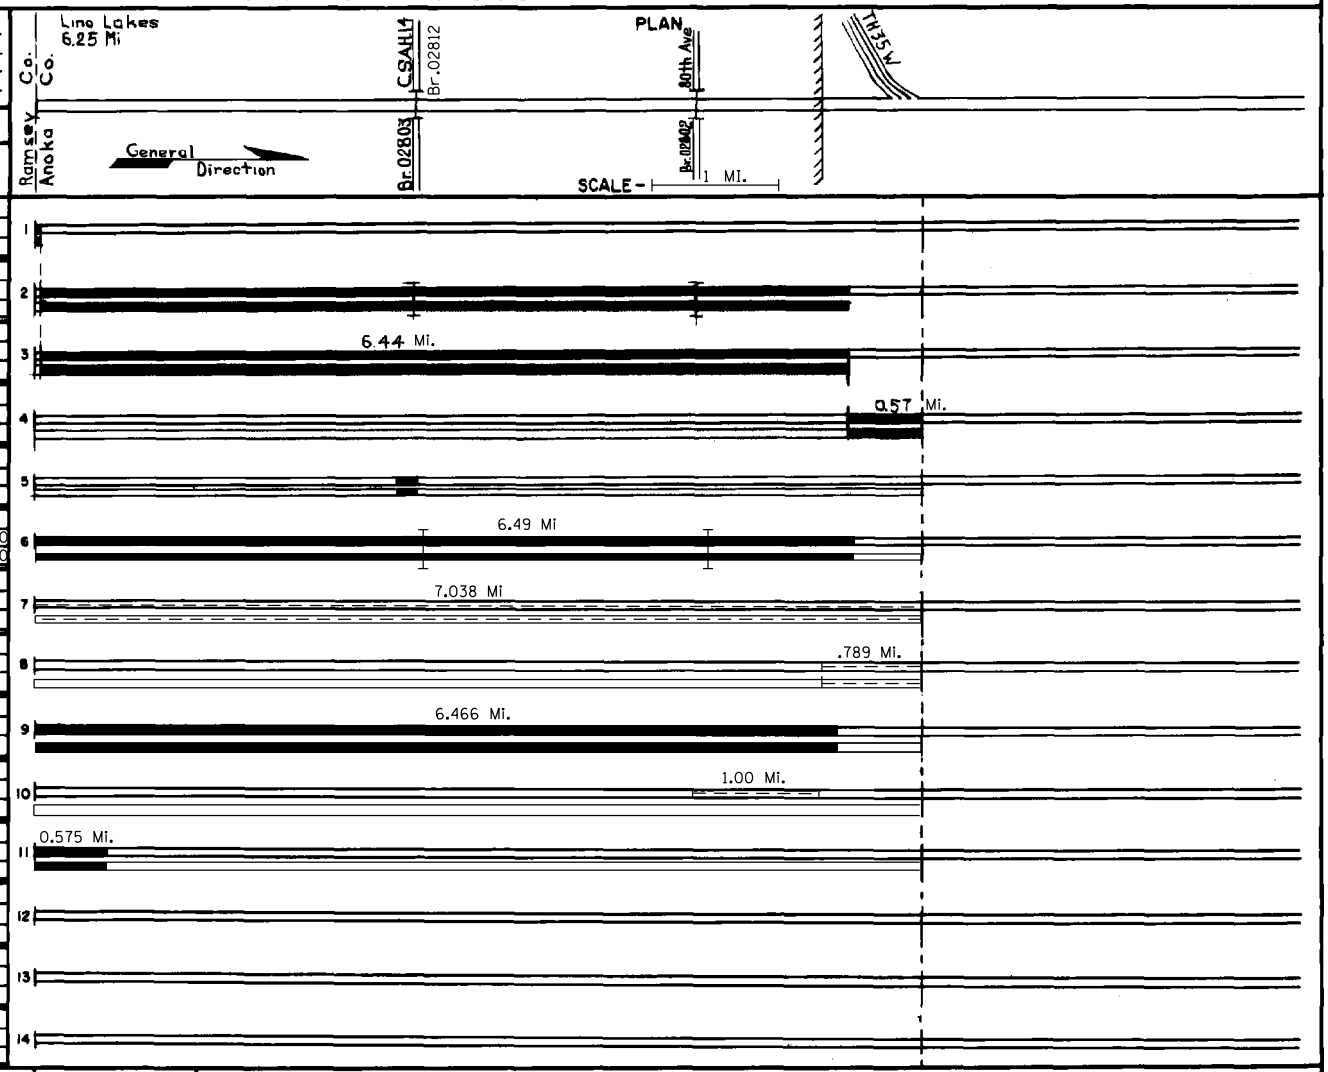

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1970		7.04	0.79	0.00	6.25	0.00	0.79	0.00	6.25	0.00

REMARKS: Layout is to scale as of 1970
