Mn/DOT 29450 (4-76)
FORM RL-7

SHEET 1 OF 1

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2771
TRUNK HIGHWAY 610
COUNTY Hennepin
DISTRICT Metro

LIMITS: Jct. ISTH-94 - E. end Br. 27239

Ref. Pt. 000+00.000 - 010+00.067

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C	0217-02	Grading at	126'		
1985	2771-03	Approaches and			
	(X 5200(2)	Br. 27239	68.3'		1326.4'
C					
1986	2771-04	Grading,			
		Bit. Surfacing			
M					
1991	M4488	Conc. Surf. Repair			
C		Grading	56-58'		
1997	2771-12	Concrete Doweled	Var.	10"	Const. Jnt. Spacing 15 Ft.
		Agg. Base	Var.	3"	Class 5
C		Concrete Doweled	27'	10"	Const. Jnt. Spacing 15 Ft.
1998	2771-15	Grading	45'		
		Agg. Base	Var.	3"	Class 5
C		Concrete Doweled	39'	10"	Const. Jnt. Spacing 15 Ft.
1998	2771-11	Grading	62'		
		Agg. Base	58'	3"	Class 5
C		Concrete Doweled	27'	10"	Const. Jnt. Spacing 15 Ft.
1999	2771-14	Grading	54-56'		
		Agg. Base	Var.	12"	
2007	8825-231	Fog Seal			
		Extension of Mainline			was 4.958 Mi.
2011	2771-38	Grading/Agg. Base	var.	var.	
		Concrete Paving	24'	12"	Non Reinforced
		Extension of Mainline			was 7.58 Mi.
2016	2771-37	Grading/Agg. Base	var.	12"	
		Conc. Surfacing	var.	var.	
		Grading			
2016	2771-106	High tension cable &			
		Plate beam Guardrail			

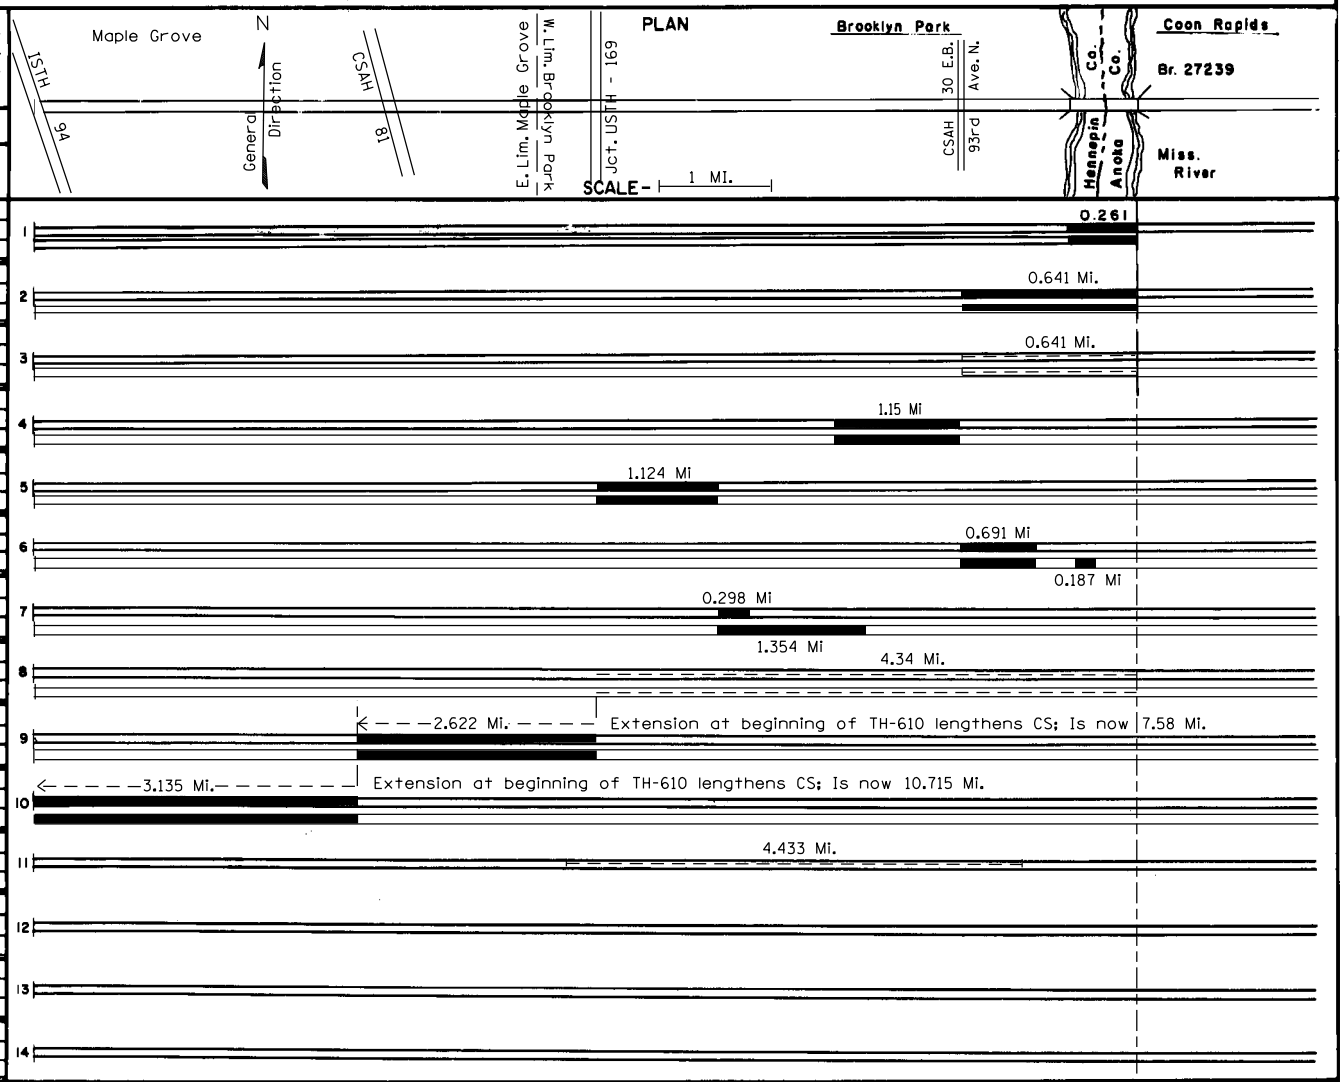

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
