FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4301
TRUNK HIGHWAY 7
COUNTY McLeod
DISTRICT 8A

LIMITS: W. Co. Line - Jct. T.H. 22

PLAN



SCALE:- 1" = ½ MI.

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
					No Record of Constr.	
		Gravel	22'	1"	Added in 1934.	
		Br. 4898	19'		45' L.T.	
M 1940	A.F.E.13	Regravelling			322 C.Y./Mile. Maint. Dept.	
M 1941	A.F.E.44	Regravelling			250 C.Y./Mile. Maint. Dept.	
M 1943	A.F.E. 6	Grav. Resurface (Spots)			205 C.Y./Mi. Maint. Dept.	
M 1945	A.F.E. 6	Grav. Resurfacing			299 C.Y./Mi. Maint. Div.	
M 1946	A.F.E. 6	Grav Resurfacing	22'		1110 C.Y.	
M 1947	A.F.E. 6	Grav. Resurfacing			1512 Tons	
M 1948	A.F.E. 6	Grav. Resurfacing			1554 Tons	
M 1951	A.F.E. 6	Grav. Resurfacing			1570 Tons	

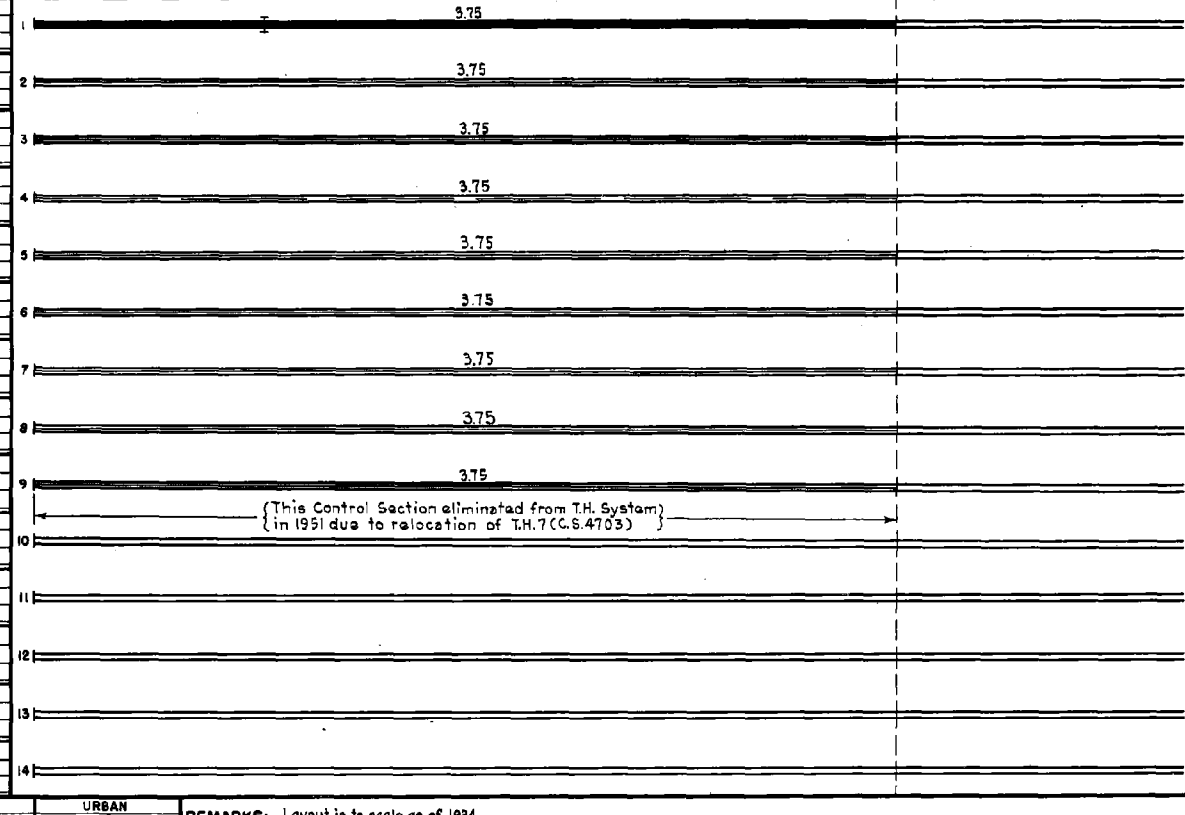

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1950	3.75	3.74	0.01	0.00	0.00	3.74	0.01	0.00	0.00
1951		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934.
