FORM R.L.-7 REV. 3-58

SHEET 1 OF 5

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

Interstate

CONTROL SECTION 6280
TRUNK HIGHWAY 35E
COUNTY Ramsey
DISTRICT 9A

LIMITS: S. end Mississippi River Bridge 9330 at Dakota-Ramsey Co. Line – E. Jct. T.H. 694



YEAR BUILT	PROJECT No.	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C		Grading	2@58'		Divided Highway
1961	6235-03	Sub-base	2@47'	16"	*AC surf on N.B. rdwy. only
	6280-79	Base & Asphaltic Conc.*	*1-24'	* 3"	Portion on ramps
C		Grading	2@56'		Divided Highway
1961	6280-03&14	Gravel Base	2@45'	4"	over 12" Sub-base
		Concrete	2@24'	10"	
C	6235-08	Br. 6513			198' B.S.-U.P.
1961	6280-05	Br. 6512			246' P.G.-U.P.
	6280-10	Br. 6579			178' P.C.G.-U.P.
C	6280-04	Br. 6511			178' P.C.G.-U.P.
1961	6280-07	Br. 6514			178' P.C.G.-U.P.
	6280-18	Br. 6509 & 6510	52'-52'		both 129' P.C.G.-O.H.
C	6280-15	Br. 9117 & 9118	54'-54'		both 139' P.C.G.-O.H.
1961	6280-16	Br. 9119 & 9120	51'-51'		both 192' P.C.G.-O.H.
	6280-17	Br. 6508			202' P.C.G.-U.P.
C		Bit. Base	26'	4"	On S.B. rdwy. only
1963	6280-92	Asphaltic Conc.	2-24'		4" On SB rdwy & 1" On N.B. rdwy.
C	6280-23	Grading			Divided Highway
1965	6280-9330 A&B	Br. 9330	2@29'		1406' P.G. & B.S.-O.H.
	6280-9534	Br. 9534	2@36'		96' P.P.G.-O.H.
C		Grading Select gran*		*9"-12"	Divided Highway
1965	6280-77(1)	Gravel Base		3"	
		P.C. Concrete	2@24'	10"	
C	6280-9532	Br. 9532			131' P.G.-U.P.
1965	6280-9832	Br. 9832			171' P.P.G.-U.P.
	6280-9531	Br. 9531			225' P.P.G.-U.P.
C	6280-87&60	Grading			Divided Highway
1965	6280-9265	Br. 9265	52'-54'		164' B.S.-O.H.
	6280-6517	Br. 6517	2@54'		297' B.S.-O.H.
C		Gravel & Bit. Base		18"&4½"	2@12' lane Const. inside
1965	6280-107(2)	Asphaltic Conc.	2@36'	3½"	for widening
C	6280-6515	Br. 6515	2@42'		1285' B.S.-O.H.
1965	6280-6513	Repair Br. 6513			
C		Grading			Divided Highway
1967	6280-106	Base		6"-22½"	
		P.C. Conc. & Asphaltic Conc.		10"&3½"	
C		Grading			Divided Highway
1967	6280-96	Base		6"	
		P.C. Concrete	52'-56'	10"	

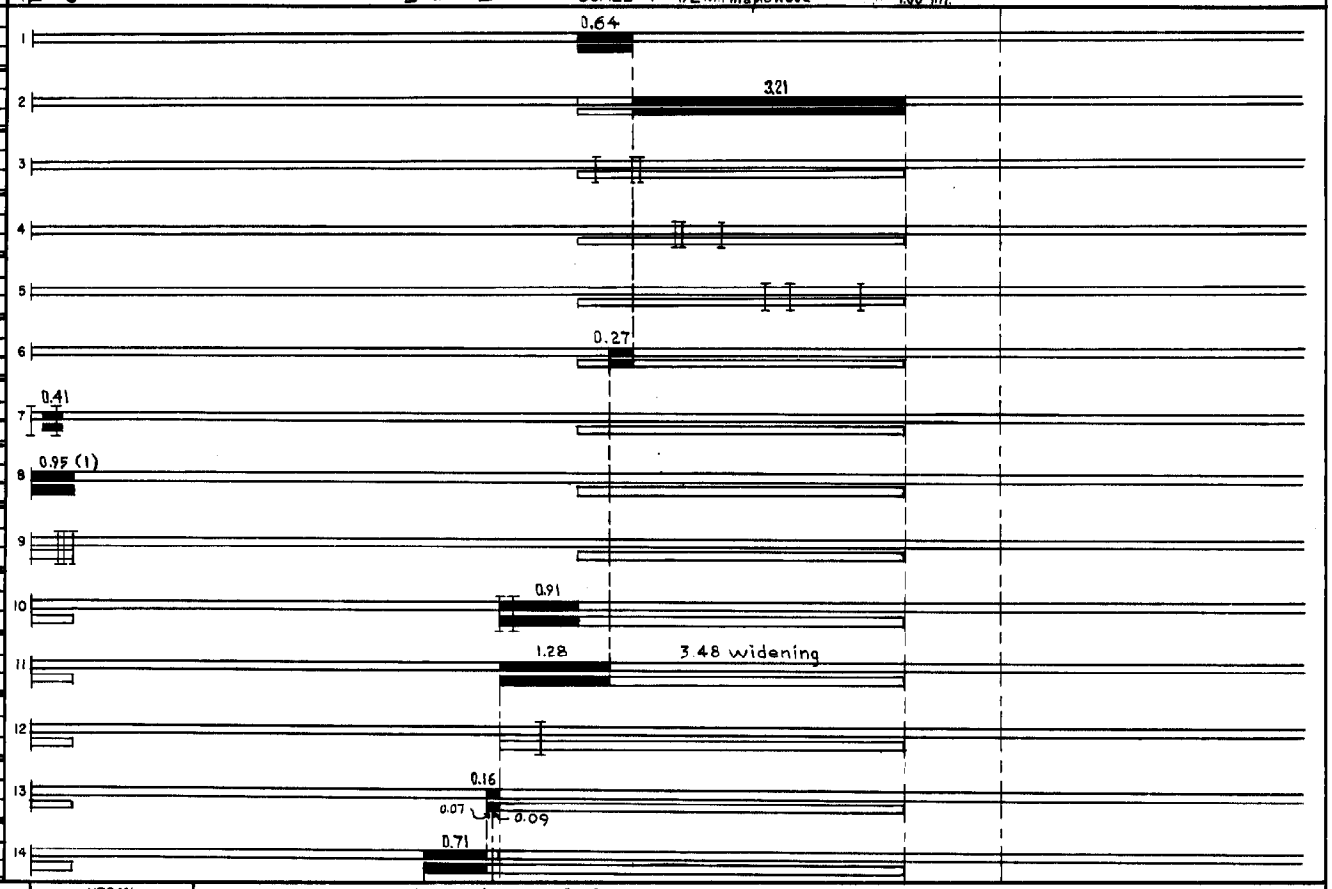

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1961	1964	3.64	0.00	0.00	3.55	0.09	0.00	0.00	3.55	0.09
1965	1966	5.72	0.00	0.00	5.02	0.70	0.00	0.00	5.02	0.70
1967	1969	6.64	0.00	0.00	5.80	0.84	0.00	0.00	5.80	0.84
1970		7.88	0.00	0.00	7.00	0.88	0.00	0.00	7.00	0.88

REMARKS: Layout is to scale as of 1961.
(1) The 0.95 mi. includes 0.12 mi. not in use graded not surfaced, 0.13 mi. temp. conn. used.
(2) P.C. conc. const. from Br. 6517 to Br. 6515.

10-74

FORM R.L.-7 REV. 3-58

SHEET 2 OF 5

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6280
Interstate TRUNK HIGHWAY 35E
COUNTY Ramsey
DISTRICT 9A

LIMITS: S. end Mississippi River Bridge 9330 at Dakota-Ramsey Co. Line — E. Jct. T.H. 694



YEAR BUILT	PROJECT NO	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C	6280-109	Grading			Divided Highway
1967	6280-97	Grading, Select gran. Base			9" Select gran., 3" gravel base
		P.C. Concrete	52'-96'	10"	
C	6280-9647	Br. 9647			233' C.B.G. - U.P.
1967	6280-9597&98	Br. 9597 & 9598			Both 247' C.B.G. - U.P.
	6280-9681&49	Br. 9681 & 9649			Both 231' C.B.G. - U.P.
C	6280-9650	Br. 9650			265' C.B.G. - U.P.
1967	6280-9807&08	Br. 9808 N.B. & 9807 S.B.			533' & 254' C.B.G. - O.H.
	6280-9655&56	Br. 9656 N.B. & 9655 S.B.			168' & 169' B.S. - O.H.
C		Grading			Divided Highway
1970	6280-49	Br. 9140			231' P.P.G. - O.H.
		Br 9561			226' P.P.G. - U.P.
C	6281-03	Grading			Divided Highway
1970	6281-04	Gravel Base		3¼"	
		P.C. Concrete	2@36'	9"	Pl. Mix. Bit Shoulder
C		Gravel Base		3¼"	
1970	6280-56	P.C. Concrete	2@36'	9"	
		Pl. Mix Bit Shoulders			
M		Edgeline Seal			20,100 Lin. Ft.
1971	SF	Joint Seal			216 Lin. Ft.
C		Br. 9520			182' Plate Girder
1966	6280-101	Br. 9521			127' PPG
	I-IG 35E-4	(70) 111			
C	6280-124				
1967	I 35E-4	Br. 9528			
	(95) 104				
C		Grade			Divided Highway
1973	6280-25	Br. 9877			164' Cont. SBS
	I 35E-4	Br. 62863			273 Cont. SBS
C	(95) 104	Br. 62864			201' Cont. SBS
1973	6280-25	Br. 62865			327' Cont. SBS
C			2@		
1973	6280-169	Bit. Overlay	36'	1"	
C					
1972	-160	TRAFFIC SIGNALS			AT C.S.A.H. 31 (MARYLAND AVE.)
	135E 4(97)109				
C					AT MARYLAND AVE., WHEELOCK
1972	-168	TRAFFIC SIGNALS			PARKWAY, ROSELAWN AVE.
	135E-4(94)109				T.H. 36, LITTLE CANADA RD.

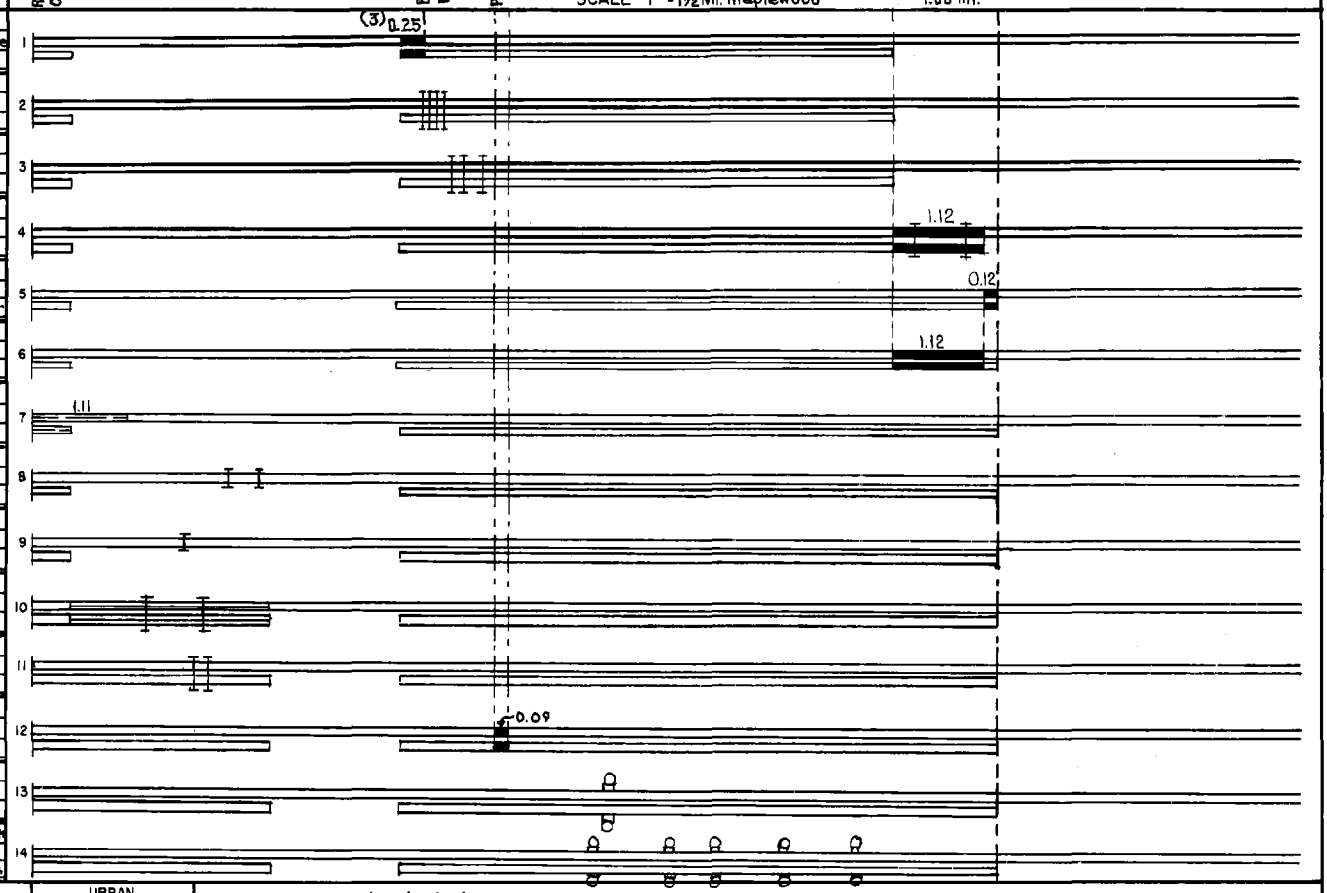

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS: See sheet No. 1
(3) 0.20 mi. included in the 0.25 mi. not in use in 1967.

10-75

Mn/DOT 29450 (4-78)
FORM RL-7

SHEET 3 OF 5

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6280
TRUNK HIGHWAY 35E
COUNTY Ramsey
DISTRICT Metro

LIMITS: S. end Mississippi River Bridge 9330 at Dakota-Ramsey Co. Line — E. Jct. T.H. 694

Ref. Pt. 102+00.597 - 114+00.104

YEAR BUILT	PROJECT NO	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C		Concrete Median			
1977	6280-214	Barrier Const.	12		
C					
1977	-159	Traffic Control Signal System			At CSAH 30 (Larpenteur Av) E & W. Ramps
C					
1978	-200	Traffic Control Signal System			At CSAH 21 (Little Canada Rd)
C	6280-186	Conc. Median Barrier.			Asph. Cem. 270 Ton
1976	TIGLUG 35E -4(101) 109	(Jersey Type) & Shldrs. And Bit. Overlay	10' 2@36'	1 3/4"	Wearing Course Spec #2361 3574 Ton
C					
1967	6280-125	Grading, Base Br 9519			At St. Clair Av 290' PCC BS
C					
1980	6280-200	Traffic Control Signals			At Little Canada Rd. (E. and W. Ramps) at Larpenteur Ave.
M					Contract No. 3953
1982	SF	Sawing Conc. Pvmt. Joints			
C		Grading, Agg. Base	Var.	6"	SP 2211 . CL-6
1984	6280-244	Bituminous Surfacing	Var.	4.5"	3 3/4" SP 2331 3/4" SP 2361
C		Br. 9534			
1984	1982-101	Deck Repair Railing Replacement			
C		Br. Repair &			
1984	6280-952	Overlay on 9521, 62863, 64, 65			
C					
1984	6280-62872	Br. 62872			Ped. Br. at Bayard Ave.
C		Milling	2-36'	2"	Remove Surface
1984	6280-242	Bit. Surfacing Ramp Overlay	2-36'	2"	1"-2331, 1"-2361
C				3 1/2"	Spec. 2331
1985	6280-230	Grading Bit. Surfacing	Var.	1/2"	Spec. 2361
C					
1986	6280-255	Conc. Repair			



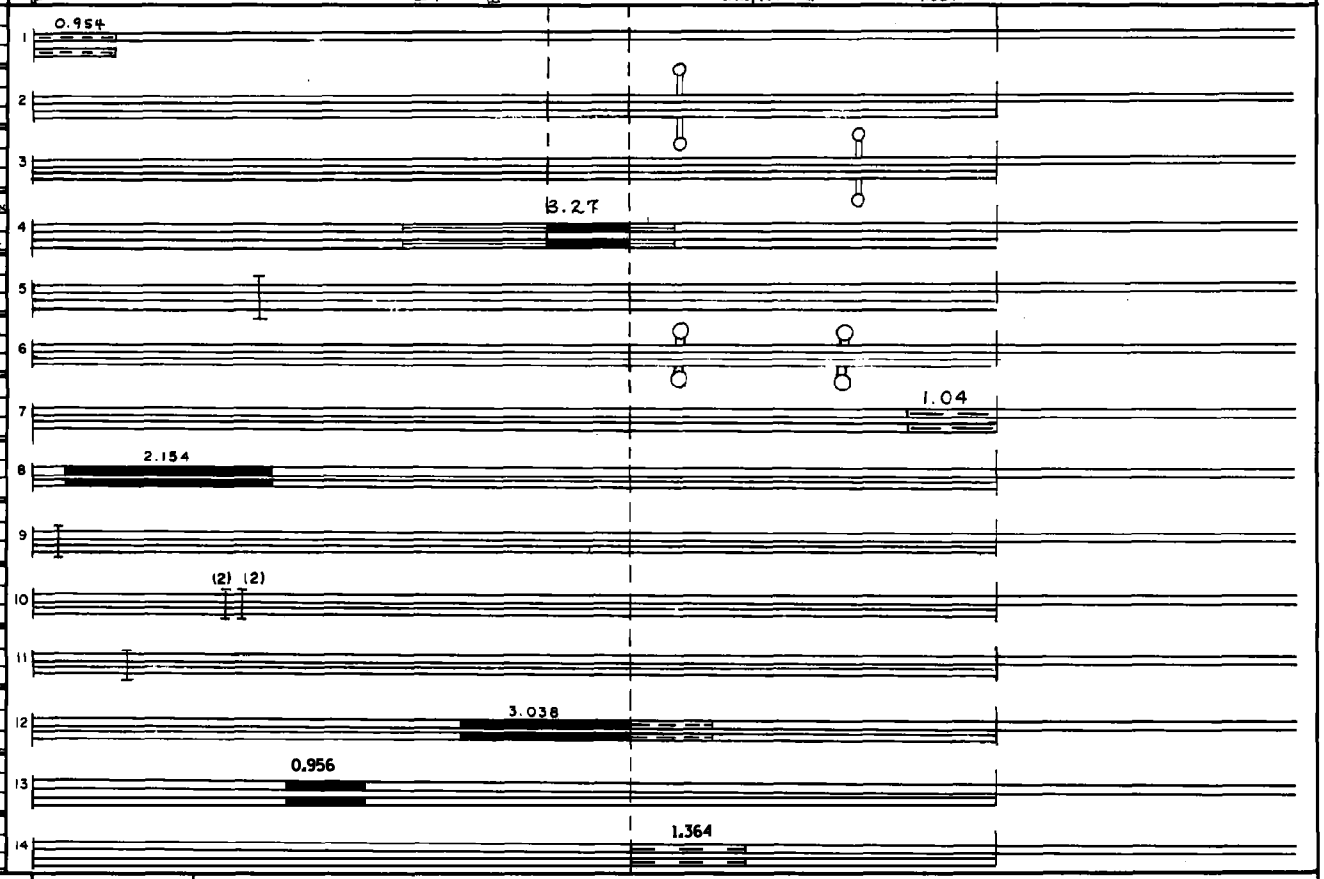

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6280
TRUNK HIGHWAY 35E
COUNTY Ramsey
DISTRICT Metro

LIMITS: Dakota/Ramsey Co. Line - E. Jct. ISTH-694

Ref. Pt. 102+00.597 - 114+00.104

YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C		Grading		3 ¾"	Spec. 2331
1986	6280-229	Bit. Surfacing	38'	¾"	Spec. 2361
C		Grading		Var.	Spec. 2331
1989	6280-251	Bit. Surfacing		1"	Spec. 2361
C		Grading		Var.	Spec. 2331
1989	6280-231	Bit. Surfacing	Var.	1"	Spec. 2361
C		Grading			
1989	6280-232	Conc. Surfacing	43'	10 ½"	
C					
1990	6280-252	Concrete Rehab.			
C				3 ½"	Spec. 2341
1992	6280-278	Bit. Overlay	Var.	1"	Spec. 2361
C					
1992	6280-279	Mill & Bit. Overlay	24'	2 ½"	Spec. 2341
C		Grading		1 ½"	Spec. 2341
1992	6280-277	Bit. Overlay	36'	1"	Spec. 2361
C					
1995	6280-276	Joint Repair			
M					
1995	M95036	Major Crack Repair			
M					
1996	8809-194	Major Crack Repair			
C		Bit. Milling	24'	2"	Spec. 2361
1998	6280-305	Bit. Overlay	24'	4"	At BR# 6514, 6579
		Conc. Rehab.			
D					
2001	8825-102	Rout & Seal			Spec. 3725
S		Grading	44'		
2004	6280-307	Concrete Surfacing	24'	10"	
		Bridge			Culvert 62X02

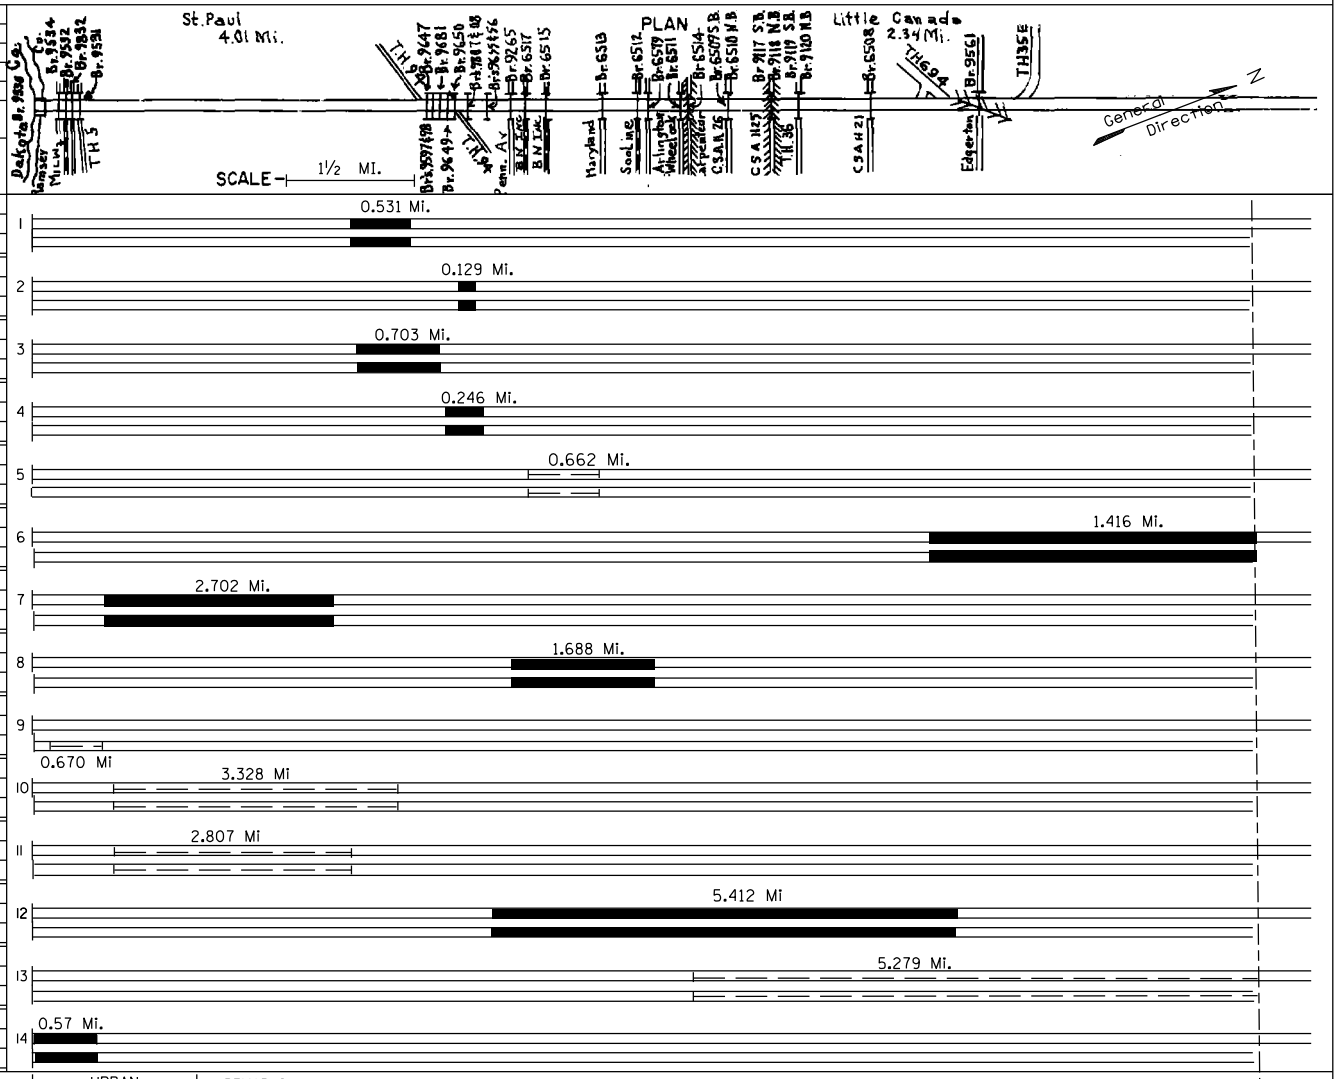

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:

FORM RL-7

SHEET 5 OF 5

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6280
TRUNK HIGHWAY 35E
COUNTY Ramsey
DISTRICT Metro

LIMITS: Dakota/Ramsey Co. Line - East Jct. ISTH-694

Ref. Pt. 102+00.597 - 114+00.104



YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	
S						
2006	6280-332	Conc. Pav. Rehab.				1
S		Grading				
2008	6280-304	Concrete surfacing	var.	10 ½"		2
S		Milling	var.	5"		
2008	6280-320	Bit. Overlay	var.	5"	Spec. 2360	3
S						
2010	6280-366	Ultra Thin Bonded			Type 2356	4
		Wear Course				
M						
2010	8825-378	Bit. Fog Seal			Seal coat shldrs only	5
S		Milling	var.	var.		
2011	6280-352	Bit. Overlay	var.	var.	Spec. 2360	6
S		Design Build TH 35E			Replace Br #6513	
2012	6280-353	Grading & Surfacing			with Br. 62626 SB	7
	(1982-150)	Ramps & shoulder	work			
S		Grading			Reconst. Outside Bus shldr	
2012	6280-359	Bit. Mill 2" & Overlay	var.	5"	Spec 2360 SB	8
		Agg. Base	var.	6"	Shoulder work	
C		Grading			Constr. MNPass	
2015	6280-367	Surface			I-35E extension	9
		Replace Bridges			Design - build	
S		Bit. Mill & Ovly			Spec. 2360	
2016	6280-369	Approach panels			Br. 9528,9519	10
					Br.62802,62803	
C		Grading/Agg. base	var.		MnPass Widening	
2016	6281-47	Bit. Surfacing	var.	7"	Spec. 2360	11
		Conc. Surfacing	var.	9"		
S		Bit. & Conc. Surfacing	var.	var.	on shldrs NB & SB	
2017	6280-390	Concrete Surfacing	24'	10"	non-reinforced	12
		Br.9534		&	conc. median & C/G 35E	
						13
						14

0.855 Mi.
2.439 Mi.
3.459 Mi.
3.54 Mi.
1.616 Mi.
0.569 Mi.
0.341 Mi.
0.637 Mi.
4.884 Mi.
1.42 Mi.
0.026 Mi.

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
